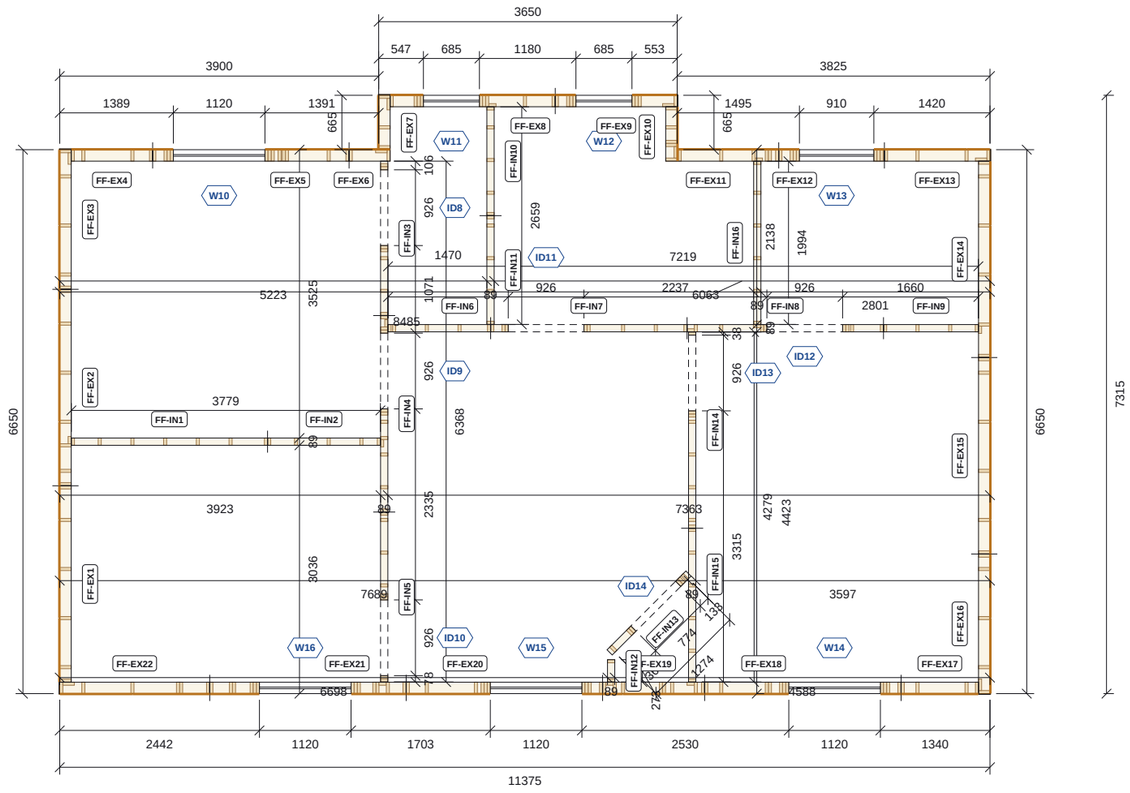


FIRST FLOOR GENERAL ARRANGEMENT PLAN

Scale 1:75 @ A3 | Plan cut at 1200 above floor deck

Timber frame panel, studs cut at plan level

Panel joint

9mm OSB/3 sheathing

Beam / steel over, set out as dimensioned

0 1 2 3 4 5m

Do not scale. All dimensions in mm. Check all dimensions on site.

FIRST FLOOR SCHEDULES

HEAD BINDER

Section	Pieces	Run m	4.8m lengths
38x140 C16	12	36.8	10

External and load-bearing walls only. Cut-optimised 4.8m stock, 3mm kerf, +5%.

TEMPORARY BRACING (NOT SHOWN)

Item	No.	Order
Brace 4x1 treated rough-sawn, 2.7m	14	8 x 5.4m
Noggin 38x89 C16, 600	14	3 x 4.8m

One brace per panel joint on external / load-bearing walls (14 joints). 2 braces per 5.4m; +5%.

WINDOW BATTENS 38X43

Item	Qty	Order
Battens (head, sill, jambs)	28 / 32.1m	8 x 4.8m 38x43
Ripped from 38x89 C16 4.8m	2 per length	4 x 4.8m 38x89

External openings only. Head/sill = width + 76; jambs = height. Cut-optimised, 3mm kerf, +5%.

OPENING SCHEDULE

Label	Width	Height	Head
W10	1120	1187	2050
W11	685	1187	2050
W12	685	1187	2050
W13	910	1187	2050
W14	1120	1337	2050
W15	1120	1337	2050
W16	1120	1337	2050

Label	Width	Height	Head
ID8	926	2050	2050
ID9	926	2050	2050
ID10	926	2050	2050
ID11	926	2050	2050
ID12	926	2050	2050
ID13	926	2050	2050
ID14	774	2050	2050

Structural opening sizes. Head level above underside of panel bottom rail.

NOTES

1. Panels: 38x140 C16 studs at 600 centres, 9mm OSB/3 to the external face (external and load-bearing walls); 38x89 C16 partitions. Panel marks refer to the manufacture drawings.
2. Head binder 38x140 C16 over external and load-bearing walls only; joints staggered from panel joints.
3. Temporary bracing (not shown): one 2.7m 4x1 treated brace at every panel joint of external and load-bearing walls, through a 600 38x89 noggin nailed to the deck.
4. Window battens 38x43 to external openings: head and sill run over the jambs by 38; doors head and jambs.
5. Steel over (dark blue, TLS supply) set out as dimensioned; TOS = top of steel above top of 22mm deck. Attic trusses and cut roof members over by Acorn Timber Engineering, see P4-RF-02. Dimensions to timber frame faces. Read with P4-FL-01 and engineer's drawing 26-431-S-0010.

REVISIONS

REV	DATE	DESCRIPTION
C01	14.09.26	Construction issue
C02	14.09.26	Roof trusses revised; SP diagonals added

TLS TIMBER FRAME DESIGN SUITE

TLS TIMBER FRAME

Design & Manufacture

Scan: 3D model + drawings

CLIENT	PROJECT
MP Adams	MP Adams Plot 4, Eckington

DRAWING TITLE

FIRST FLOOR GENERAL ARRANGEMENT

Panels, openings and steel over

SCALE	SIZE	DATE	DRAWN
1:75	A3	14.09.26	TS

STATUS	DRAWING No.	REV
CONSTRUCTION	P4-GA-02	C02
