

DETAIL 1 - ETFSS HOLDING DOWN STRAP

Engineer's detail reproduced from Skyhooks 26-431-S-0010 P01 (not to scale)

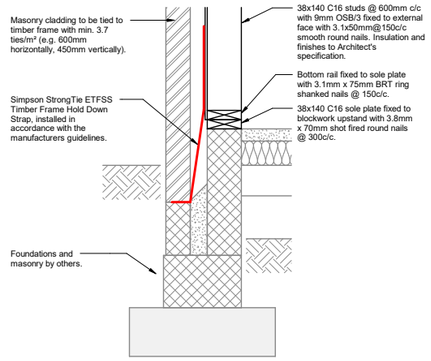

1 Plot 4 - Holding Down Strap Detail
1 : 10

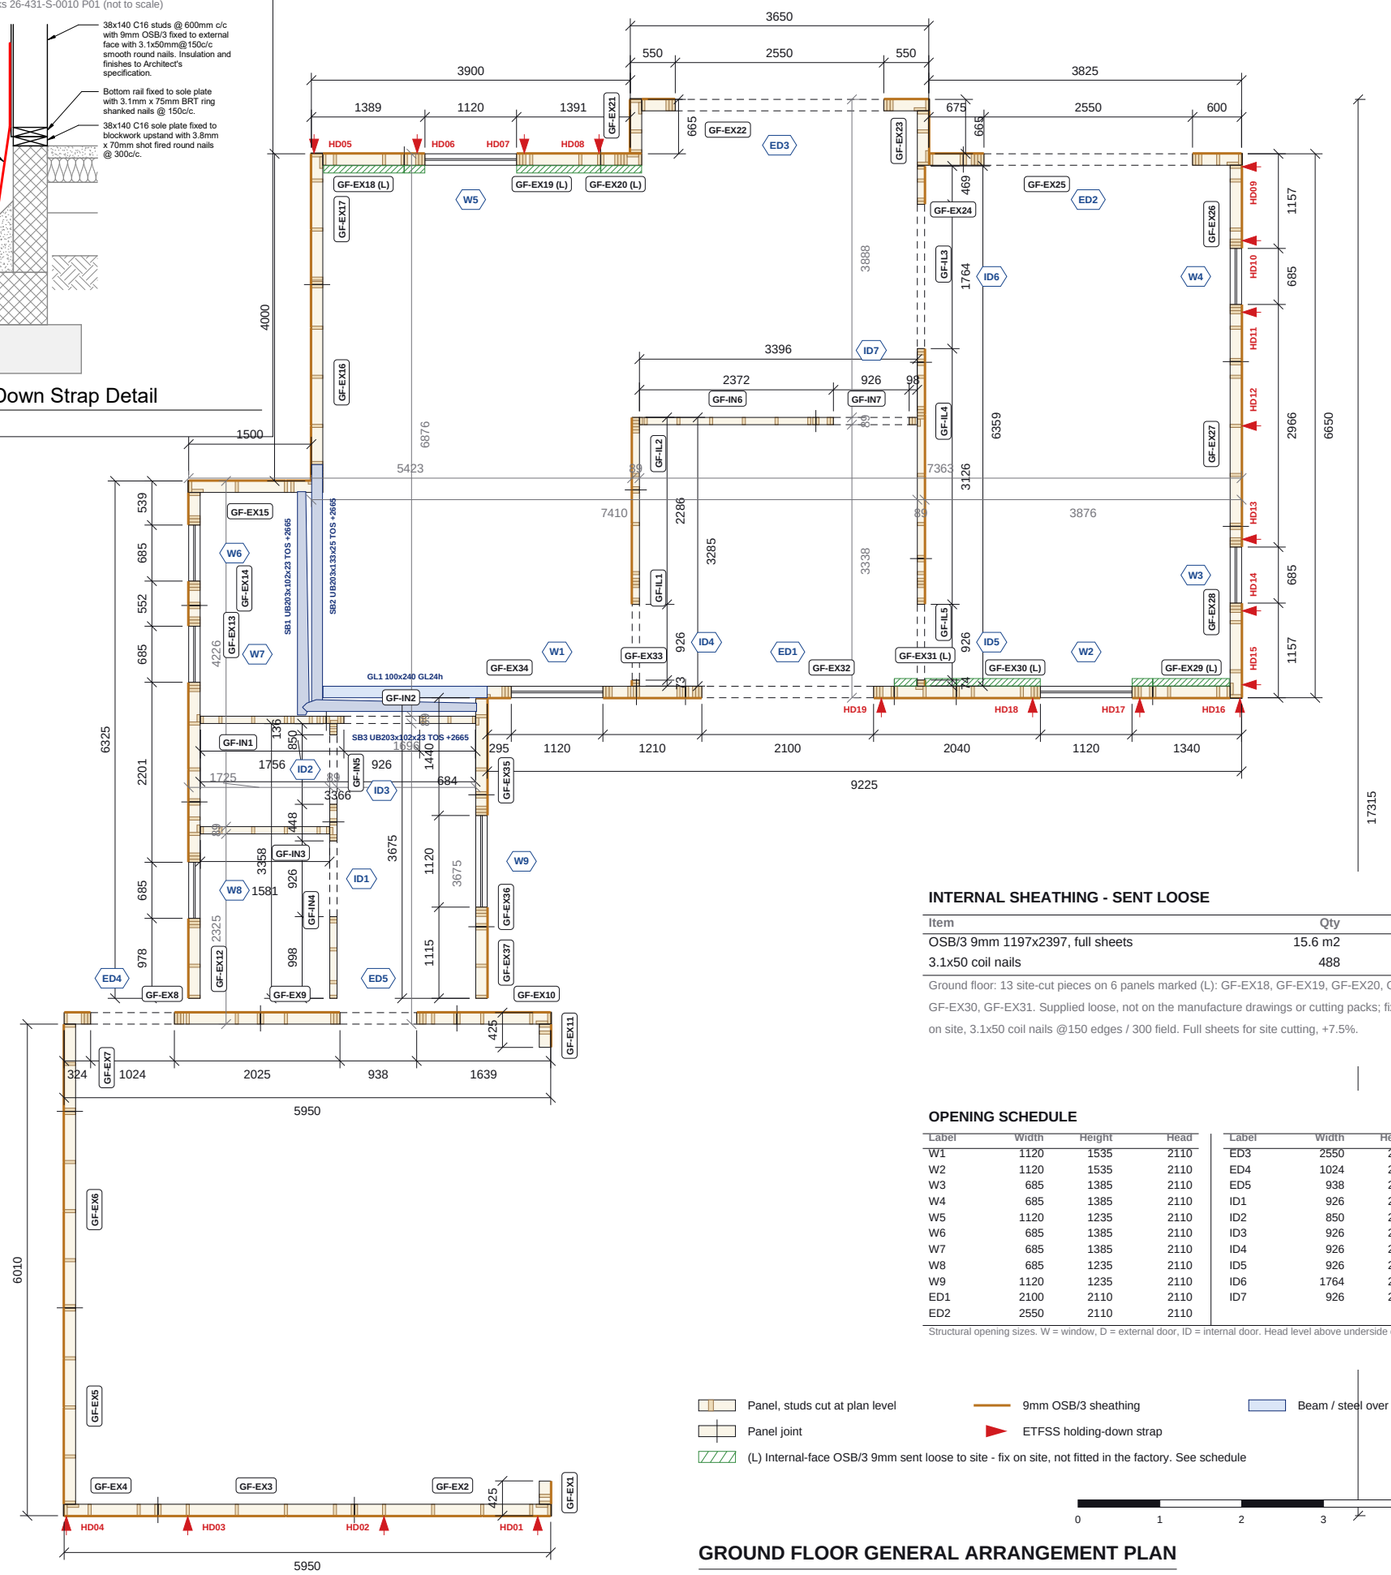

INTERNAL SHEATHING - SENT LOOSE

Item	Qty	Order
OSB/3 9mm 1197x2397, full sheets	15.6 m2	6 sheets
3.1x50 coil nails	488	1 x box 2,500

Ground floor: 13 site-cut pieces on 6 panels marked (L): GF-EX18, GF-EX19, GF-EX20, GF-EX29, GF-EX30, GF-EX31. Supplied loose, not on the manufacture drawings or cutting packs; fix to the panel studs on site, 3.1x50 coil nails @150 edges / 300 field. Full sheets for site cutting, +7.5%.

OPENING SCHEDULE

Label	Width	Height	Head
W1	1120	1535	2110
W2	1120	1535	2110
W3	685	1385	2110
W4	685	1385	2110
W5	1120	1235	2110
W6	685	1385	2110
W7	685	1385	2110
W8	685	1235	2110
W9	1120	1235	2110
ED1	2100	2110	2110
ED2	2550	2110	2110

Label	Width	Height	Head
ED3	2550	2110	2110
ED4	1024	2110	2110
ED5	938	2110	2110
ID1	926	2050	2050
ID2	850	2050	2050
ID3	926	2050	2050
ID4	926	2050	2050
ID5	926	2050	2050
ID6	1764	2050	2050
ID7	926	2050	2050

Structural opening sizes. W = window, D = external door, ID = internal door. Head level above underside of sole plate.

Panel, studs cut at plan level
Panel joint
(L) Internal-face OSB/3 9mm sent loose to site - fix on site, not fitted in the factory. See schedule
9mm OSB/3 sheathing
ETFSS holding-down strap
Beam / steel over

0 1 2 3 4 5m

GROUND FLOOR GENERAL ARRANGEMENT PLAN

Scale 1:75 @ A3 | Plan cut at 1200 above slab

GROUND FLOOR SCHEDULES

HEAD BINDER

Section	Pieces	Run m	4.8m lengths
38x89 C16	3	9.6	4
38x140 C16	25	61.3	14

External and load-bearing walls only. Cut-optimised 4.8m stock, 3mm kerf, +5%.

TEMPORARY BRACING (NOT SHOWN)

Item	No.	Order
Brace 4x1 treated rough-sawn, 2.7m	24	13 x 5.4m
Noggin 38x89 C16, 600	24	5 x 4.8m
M7.5x100 concrete screw (2 per noggin)	48	1 box of 100

One brace per panel joint on external / load-bearing walls (24 joints). 2 braces per 5.4m; +5%.

WINDOW BATTENS 38X43

Item	Qty	Order
Battens (head, sill, jambs)	51 / 72.5m	18 x 4.8m 38x43
Ripped from 38x89 C16 4.8m	2 per length	9 x 4.8m 38x89

External openings only. Head/sill = width + 76; jambs = height. Cut-optimised, 3mm kerf, +5%.

HOLDING-DOWN STRAPS (ETFSS)

Mark	Wall	At	On
HD01	W1/1	159	junction
HD02	W1/1	2038	stud
HD03	W1/1	4438	stud
HD04	W1/1	5923	end stud
HD05	W5/3	33	end stud
HD06	W5/3	1294	king W5
HD07	W5/3	2604	king W5
HD08	W5/3	3518	end stud
HD09	W5/8	159	end stud
HD10	W5/8	1062	king W4

Mark	Wall	At	On
HD11	W5/8	1937	king W4
HD12	W5/8	3326	stud
HD13	W5/8	4713	king W3
HD14	W5/8	5588	king W3
HD15	W5/8	6491	junction
HD16	W5/9	20	end stud
HD17	W5/9	1245	king W2
HD18	W5/9	2555	king W2
HD19	W5/9	4405	king ED1

19 No. Simpson Strong-Tie ETFSS, engineer 26-431-S-0010 Detail 1. 'At' = from the wall's start corner along the external frame face.

NOTES

1. Panels: 38x140 C16 studs at 600 centres, 9mm OSB/3 to the external face (external and load-bearing walls); 38x89 C16 partitions. Panel marks refer to the manufacture drawings.
2. Head binder 38x140 C16 over external and load-bearing walls only; joints staggered from panel joints.
3. Temporary bracing (not shown): one 2.7m 4x1 treated brace at every panel joint of external and load-bearing walls, through a 600 38x89 noggin fixed with 2 No. M7.5x100 concrete screws.
4. Window battens 38x43 to external openings: head and sill run over the jambs by 38; doors head and jambs.
5. ETFSS holding-down straps (red) on the stud scheduled, to engineer's Detail 1 and Simpson guidance.
6. Beams and steel over (dark blue) set out as dimensioned; TOS = top of steel above underside of sole plate. Dimensions to timber frame faces. Read with P4-SP-01, P4-FL-01 and engineer's drawing 26-431-S-0010.

REVISIONS

REV	DATE	DESCRIPTION
C01	14.09.26	Construction issue
C02	14.09.26	Roof trusses revised; SP diagonals added
C03	11.10.26	FF windows coursed; steel + GP1 portal; steel drawings (ST)

TLS TIMBER FRAME DESIGN SUITE

TLS TIMBER FRAME
Design & Manufacture
Scan: 3D model + drawings

CLIENT	PROJECT
MP Adams	MP Adams Plot 4, Eckington

DRAWING TITLE

GROUND FLOOR GENERAL ARRANGEMENT

Panels, openings, holding-down straps, beams and steel over

SCALE	SIZE	DATE	DRAWN
1:75	A3	11.10.26	TS

STATUS	DRAWING No.	REV
CONSTRUCTION	P4-GA-01	C03

Do not scale. All dimensions in mm. Check all dimensions on site.
