

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

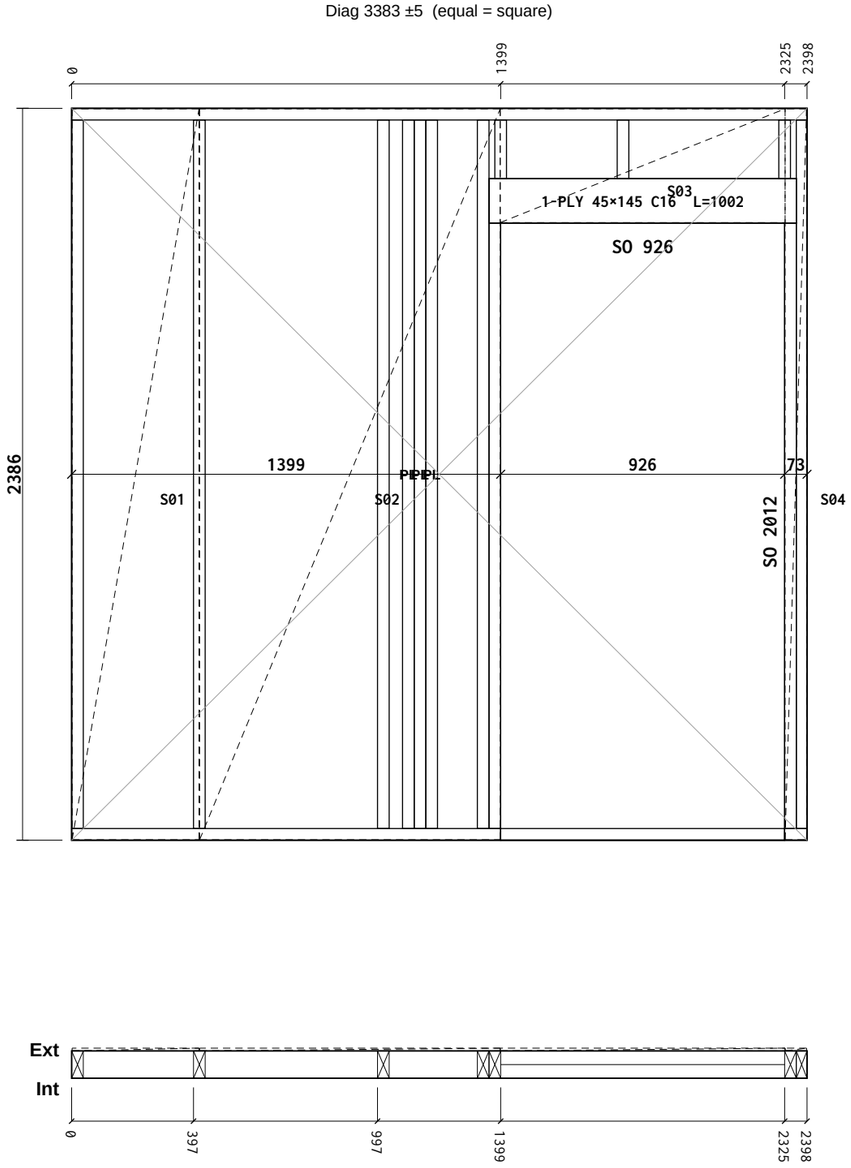



Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×89 C16	1399	0	0	1
BR2 Bottom Rail	38×89 C16	926	0	0	1
BR3 Bottom Rail	38×89 C16	73	0	0	1
TR1 Top Rail	38×89 C16	2398	0	0	1
ES1 End Stud	38×89 C16	2310	0	0	1
ES2 End Stud	38×89 C16	191	0	0	1
KS1 Vertical Stud	35×89 C16	2310	0	0	1
KS2 Vertical Stud	38×89 C16	2310	0	0	1
CS1 Cripple Stud	38×89 C16	1974	0	0	2
LP1 Lintel Ply	1002×45 C16	1002	0	0	1
PK1 Lintel Packer	1002×41 C16	1002	0	0	1
OS1 OSB Support	38×89 C16	191	0	0	2
VS1 Vertical Stud	38×89 C16	2310	0	0	2

Total: 16 pcs / 22.87 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	414	2383	**S01**
OSB 9mm	980	2383	**S02**
OSB 9mm	929	371	**S03**
OSB 9mm	70	2383	**S04**

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails


Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm

Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN

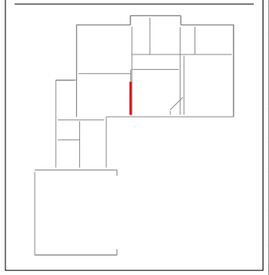


Revisions (Rev · Date · Note):


C03 - FF windows coursed; steel + GP1 portal; steel drawings (ST)


Date: **2026-10-11**	Scale: **1:20**	Drawn: **TS**	Checked:
Project Name: **MP Adams Plot 4, Eckington**			
Site: **Eckington**		Client: **MP Adams**	
Title: **Panel Fabrication — 38 x 140 C16 CLS**			
Project Number: **P4**		Revision: **C03**	
Panel No: **GF-IL1**		Drawing No: **P4-MF-GF-IL1**	
Panel L×H×T: **2398×2386×98**		Weight: **56 kg**	
Status: **CONSTRUCTION**		Sheet: **1 / 1**	

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

Diag 2545 ±5 (equal = square)

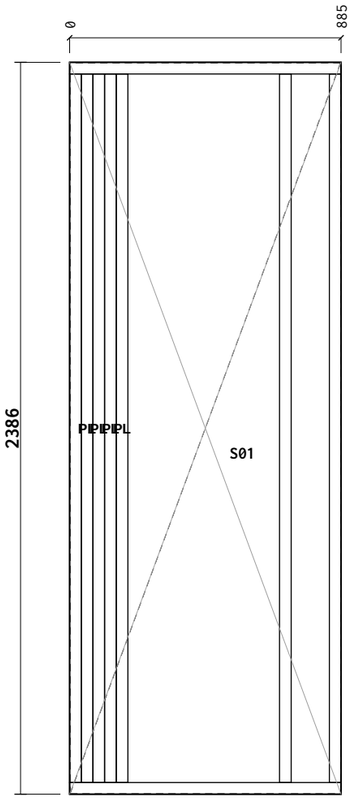





Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×89 C16	885	0	0	1
TR1 Top Rail	38×89 C16	885	0	0	1
ES1 End Stud	38×89 C16	2310	0	0	1
ES2 End Stud	38×89 C16	2310	0	0	1
VS1 Vertical Stud	38×89 C16	2310	0	0	1

Total: 5 pcs / 8.70 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	882	2383	**S01**

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails


Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm

Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN

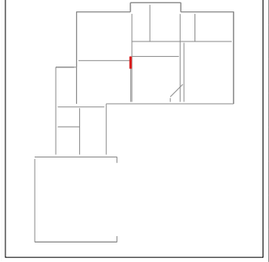


Revisions (Rev · Date · Note)


C03 - FF windows coursed; steel + GP1 portal; steel drawings (ST)

Date: **2026-10-11**	Scale: **1:20**	Drawn: **TS**	Checked:
Project Name: **MP Adams Plot 4, Eckington**			
Site: **Eckington**		Client: **MP Adams**	
Title: **Panel Fabrication — 38 x 140 C16 CLS**			
Project Number: **P4**		Revision: **C03**	
Panel No: **GF-IL2**		Drawing No: **P4-MF-GF-IL2**	
Panel L×H×T: **885×2386×98**		Weight: **24 kg**	
Status: **CONSTRUCTION**		Sheet: **1 / 1**	


Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

Diag 3384 ±5 (equal = square)

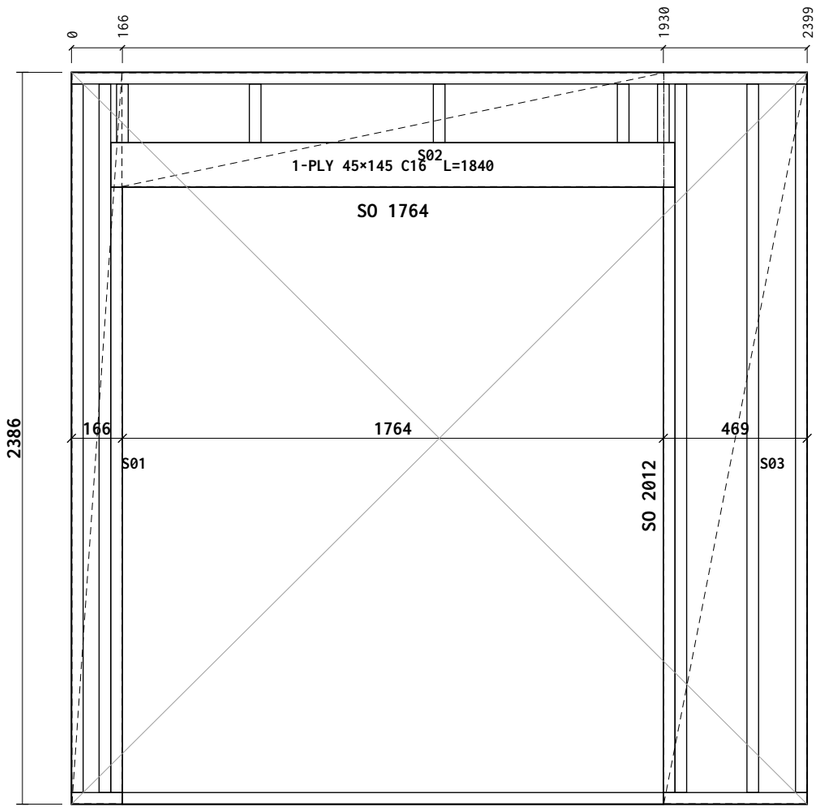



Section A-A



Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×89 C16	1764	0	0	1
BR2 Bottom Rail	38×89 C16	469	0	0	1
BR3 Bottom Rail	38×89 C16	166	0	0	1
TR1 Top Rail	38×89 C16	2399	0	0	1
ES1 End Stud	38×89 C16	2310	0	0	1
ES2 End Stud	38×89 C16	2310	0	0	1
KS1 Vertical Stud	38×89 C16	2310	0	0	2
CS1 Cripple Stud	38×89 C16	1974	0	0	2
LP1 Lintel Ply	1840×45 C16	1840	0	0	1
PK1 Lintel Packer	1840×41 C16	1840	0	0	1
OS1 OSB Support	38×89 C16	191	0	0	2
VS1 Vertical Stud	38×89 C16	2310	0	0	1
VS2 Vertical Stud	38×89 C16	191	0	0	3

Total: 18 pcs / 24.93 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	163	2383	**S01**
OSB 9mm	1767	371	**S02**
OSB 9mm	466	2383	**S03**

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails


Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm

Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN

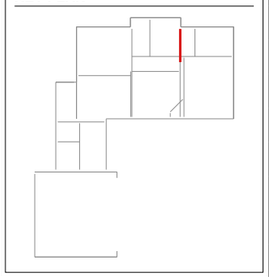


Revisions (Rev · Date · Note):


C03 - FF windows coursed; steel + GP1 portal; steel drawings (ST)

Date: **2026-10-11**	Scale: **1:20**	Drawn: **TS**	Checked:
Project Name: **MP Adams Plot 4, Eckington**			
Site: **Eckington**		Client: **MP Adams**	
Title: **Panel Fabrication — 38 x 140 C16 CLS**			
Project Number: **P4**		Revision: **C03**	
Panel No: **GF-IL3**		Drawing No: **P4-MF-GF-IL3**	
Panel L×H×T: **2399×2386×98**		Weight: **52 kg**	
Status: **CONSTRUCTION**		Sheet: **1 / 1**	


Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

Diag 3383 ±5 (equal = square)

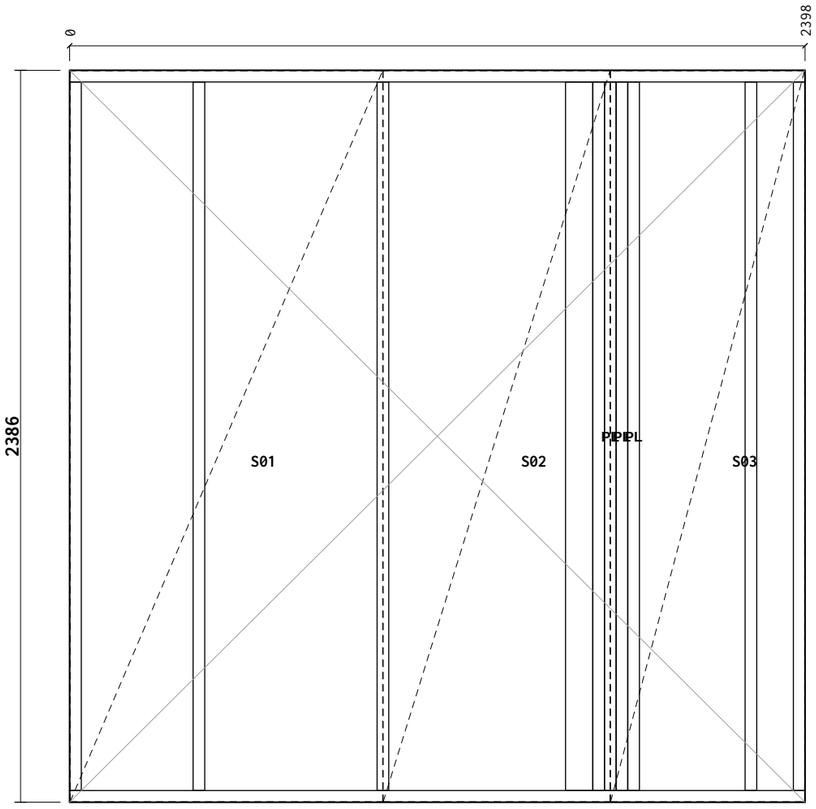



Section A-A



Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×89 C16	2398	0	0	1
TR1 Top Rail	38×89 C16	2398	0	0	1
ES1 End Stud	38×89 C16	2310	0	0	1
ES2 End Stud	38×89 C16	2310	0	0	1
VS1 Vertical Stud	38×89 C16	2310	0	0	4
JS1 Junction Stud	38×89 C16	2310	0	0	1

Total: 9 pcs / 20.97 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	1019	2383	**S01**
OSB 9mm	739	2383	**S02**
OSB 9mm	633	2383	**S03**

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails


Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm

Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN

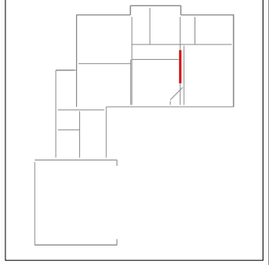



Revisions (Rev · Date · Note):


C03 - FF windows coursed; steel + GP1 portal; steel drawings (ST)

Date: **2026-10-11**	Scale: **1:20**	Drawn: **TS**	Checked:
Project Name: **MP Adams Plot 4, Eckington**			
Site: **Eckington**		Client: **MP Adams**	
Title: **Panel Fabrication — 38 x 140 C16 CLS**			
Project Number: **P4**		Revision: **C03**	
Panel No: **GF-IL4**		Drawing No: **P4-MF-GF-IL4**	
Panel L×H×T: **2398×2386×98**		Weight: **61 kg**	
Status: **CONSTRUCTION**		Sheet: **1 / 1**	

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

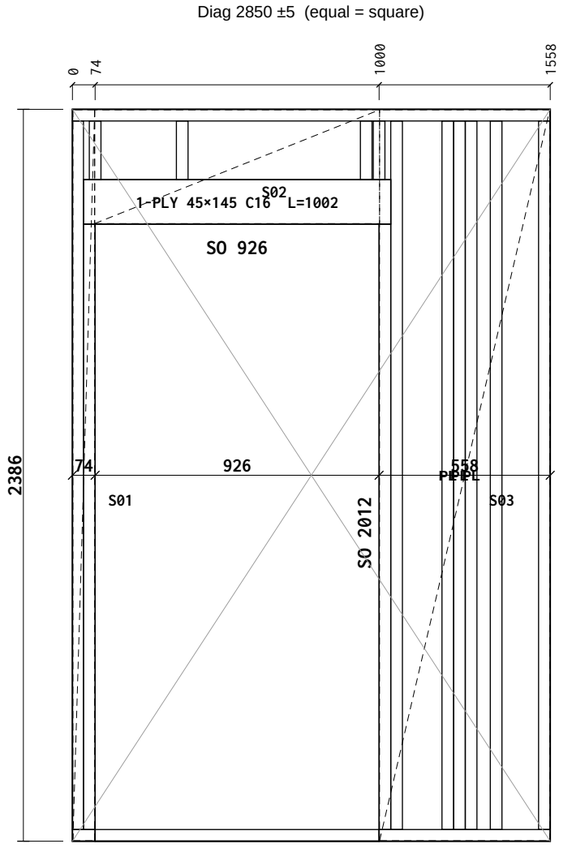





Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×89 C16	926	0	0	1
BR2 Bottom Rail	38×89 C16	558	0	0	1
BR3 Bottom Rail	38×89 C16	74	0	0	1
TR1 Top Rail	38×89 C16	1558	0	0	1
ES1 End Stud	38×89 C16	191	0	0	1
ES2 End Stud	38×89 C16	2310	0	0	1
KS1 Vertical Stud	38×89 C16	2310	0	0	1
KS2 Vertical Stud	36×89 C16	2310	0	0	1
CS1 Cripple Stud	38×89 C16	1974	0	0	2
LP1 Lintel Ply	1002×45 C16	1002	0	0	1
PK1 Lintel Packer	1002×41 C16	1002	0	0	1
OS1 OSB Support	38×89 C16	191	0	0	2
VS1 Vertical Stud	38×89 C16	2310	0	0	1
VS2 Vertical Stud	38×89 C16	191	0	0	1

Total: 16 pcs / 19.07 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	71	2383	**S01**
OSB 9mm	929	371	**S02**
OSB 9mm	555	2383	**S03**

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails


Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm

Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN

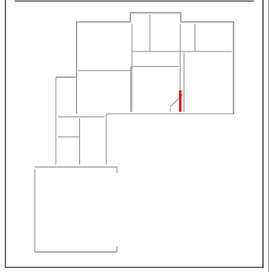

Revisions (Rev · Date · Note):

C03 - FF windows coursed; steel + GP1 portal; steel drawings (ST)

Date: **2026-10-11**	Scale: **1:20**	Drawn: **TS**	Checked:
Project Name: **MP Adams Plot 4, Eckington**			
Site: **Eckington**		Client: **MP Adams**	
Title: **Panel Fabrication — 38 x 140 C16 CLS**			
Project Number: **P4**		Revision: **C03**	
Panel No: **GF-IL5**		Drawing No: **P4-MF-GF-IL5**	
Panel L×H×T: **1558×2386×98**		Weight: **39 kg**	
Status: **CONSTRUCTION**		Sheet: **1 / 1**	
