

PLAN SECTION SC2 1:10

plan at +1231 (through-bolt height), north up

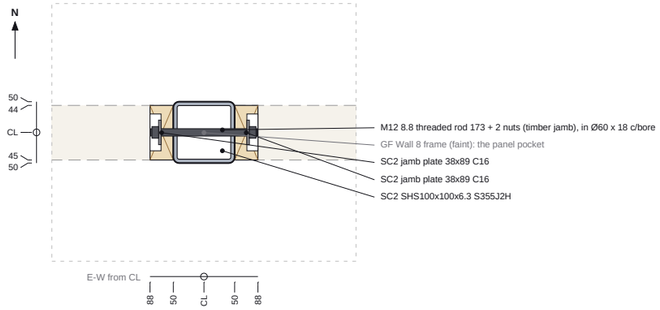

PLAN SECTION SC3 1:10

plan at +1231 (through-bolt height), north up

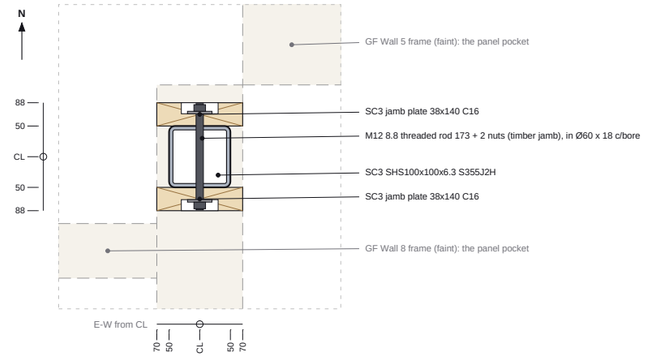

PLAN SECTION PC1 1:10

plan at +1150 (through-bolt height), north up

PLAN SECTION PC2 1:10

plan at +1150 (through-bolt height), north up

NOTES

1. **FOR APPROVAL - NOT FOR FABRICATION until the engineer has approved the TLS details and returned the steel drawings.**
2. Cross-sections through each member, drawn from the steel spec: steel true shape, welded plates, the TLS timber kit and its fixings in place. Faint = adjacent timber frame (construction data).
3. Stone coursing from FFL: bed joints 150n..150n+10, 140 stone units. DPC on the flange under the stone; first course made up to the coursing.
4. Counterbores as the fixing schedule (head / nut + washer below the timber face).
5. ALL STEELWORK SUBJECT TO SITE MEASURE BEFORE FABRICATION.

REVISIONS

REV	DATE	DESCRIPTION
C03	11.10.26	Steel fabrication drawings - first issue

TLS TIMBER FRAME DESIGN SUITE

TLS TIMBER FRAME

Design & Manufacture

Scan: 3D model + drawings

CLIENT	PROJECT
MP Adams	MP Adams Plot 4, Eckington

DRAWING TITLE

STEEL MEMBER SECTIONS

Sections through each member with the timber kit, fixings, stone and levels

SCALE	SIZE	DATE	DRAWN
1:10 / as noted	A3	11.10.26	TS

STATUS	DRAWING No.	REV
FOR APPROVAL	P4-ST-SEC2	C03

Do not scale. All dimensions in mm. Check all dimensions on site.
