


Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

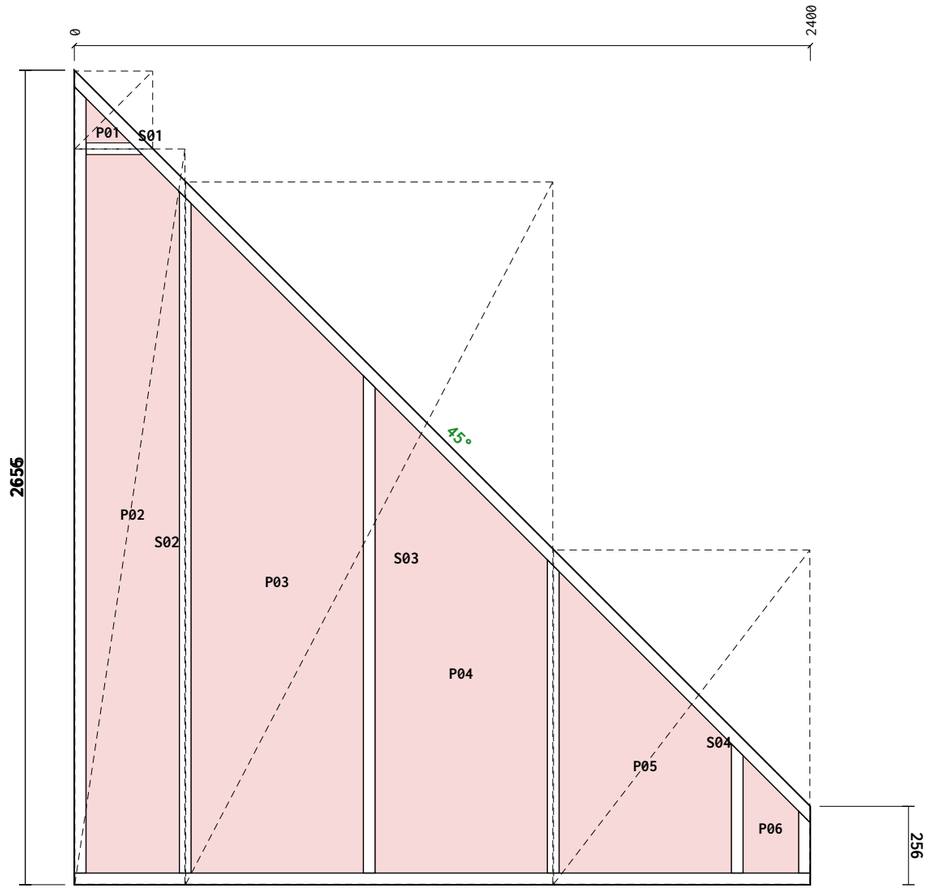

Breather bot overlap: 150mm

Breather R overlap: 150mm





Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2400	0	0	1
TR1 Top Rail	38×140 C16	2400	0	0	1
ES1 End Stud	38×140 C16	2564	0	45.0	1
ES2 End Stud	38×140 C16	202	0	45.0	1
VS1 Vertical Stud	38×140 C16	2221	0	45.0	1
VS2 Vertical Stud	38×140 C16	1621	0	45.0	1
VS3 Vertical Stud	38×140 C16	1021	0	45.0	1
VS4 Vertical Stud	38×140 C16	421	0	45.0	1
NG1 Noggin	38×140 C16	182	0	0	1

Total: 9 pcs / 13.03 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	254	254	**S01**
OSB 9mm	359	2397	**S02**
OSB 9mm	1197	2289	**S03**
OSB 9mm	836	1090	**S04**
PIR 120mm	145	144	**P01**
PIR 120mm	304	2342	**P02**
PIR 120mm	561	2182	**P03**
PIR 120mm	561	1582	**P04**
PIR 120mm	561	982	**P05**
PIR 120mm	180	382	**P06**

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.


Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.


KEY PLAN

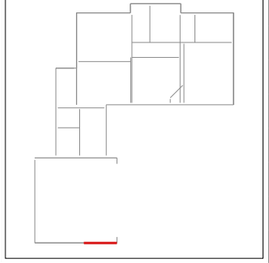

Revisions (Rev · Date · Note):	C01 - Construction issue		
Date: 2026-09-14	Scale: 1:20	Drawn: TS	Checked:
Project Name:	MP Adams Plot 4, Eckington		
Site: Eckington		Client: MP Adams	
Title:	Panel Fabrication — 38 x 140 C16 CLS		
Project Number: P4		Revision: C01	
Panel No: GB-EX1		Drawing No: P4-MF-GB-EX1	
Panel L×H×T: 2400×2655×149		Weight: 410 kg	
Status: CONSTRUCTION		Sheet: 1 / 1	

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

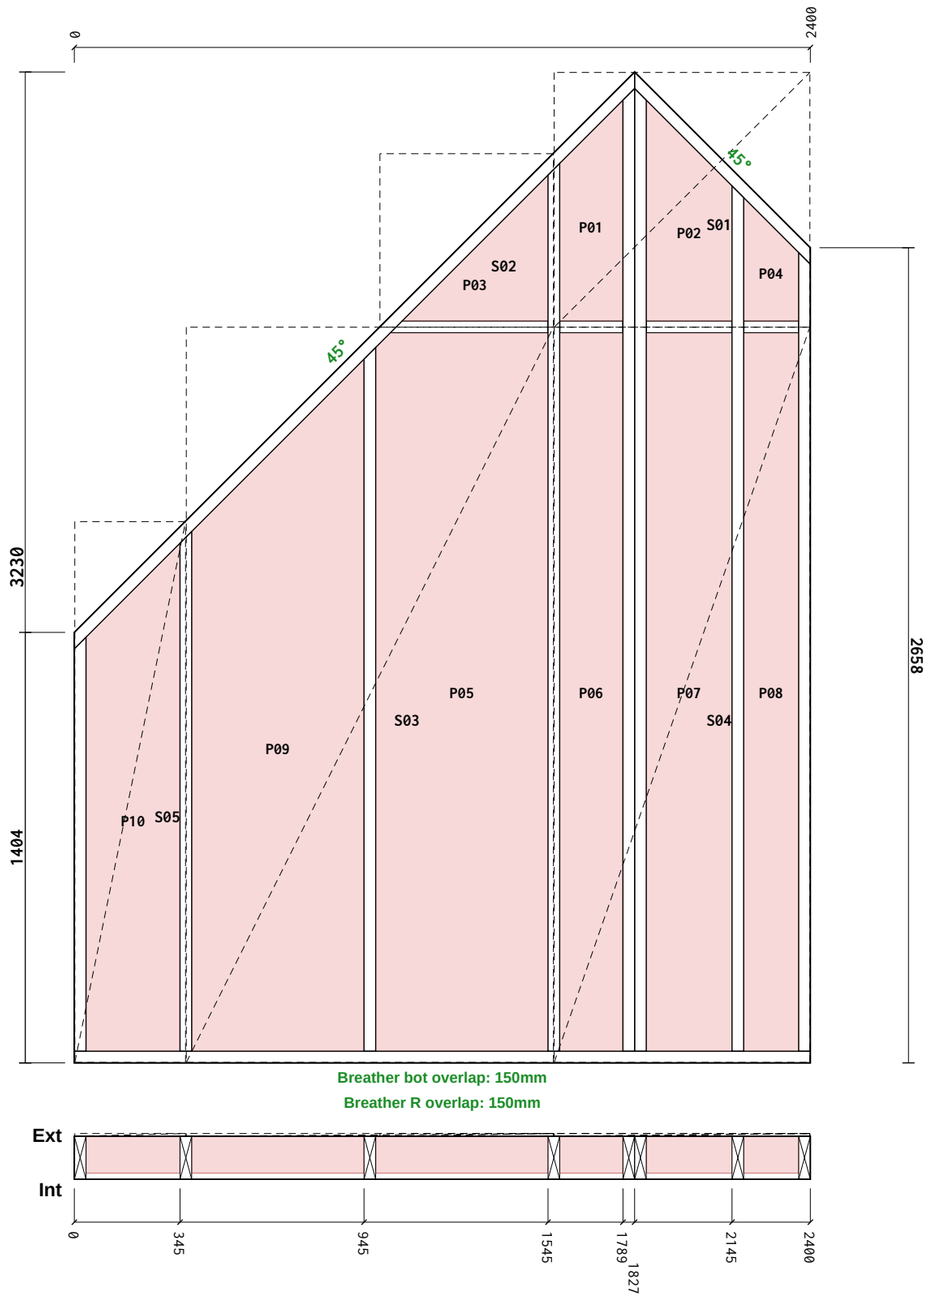



Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2400	0	0	1
TR1 Top Rail	38×140 C16	1827	0	0	1
TR2 Top Rail	38×140 C16	573	0	0	1
ES1 End Stud	38×140 C16	1350	0	-45.0	1
ES2 End Stud	38×140 C16	2604	0	45.0	1
VS1 Vertical Stud	38×140 C16	3139	0	45.0	1
VS2 Vertical Stud	38×140 C16	3139	0	-45.0	1
VS3 Vertical Stud	38×140 C16	2894	0	-45.0	1
VS4 Vertical Stud	38×140 C16	2821	0	45.0	1
VS5 Vertical Stud	38×140 C16	2294	0	-45.0	1
VS6 Vertical Stud	38×140 C16	1694	0	-45.0	1
NG1 Noggin	38×140 C16	513	0	0	1
NG2 Noggin	38×140 C16	278	0	0	1
NG3 Noggin	38×140 C16	204	0	0	1
NG4 Noggin	38×140 C16	177	0	0	1

Total: 15 pcs / 25.91 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	834	830	**S01**
OSB 9mm	566	566	**S02**
OSB 9mm	1197	2397	**S03**
OSB 9mm	834	2397	**S04**
OSB 9mm	361	1763	**S05**
PIR 120mm	205	719	**P01**
PIR 120mm	279	719	**P02**
PIR 120mm	475	475	**P03**
PIR 120mm	178	402	**P04**
PIR 120mm	561	2342	**P05**
PIR 120mm	205	2342	**P06**
PIR 120mm	279	2342	**P07**
PIR 120mm	178	2342	**P08**
PIR 120mm	561	2255	**P09**
PIR 120mm	306	1655	**P10**

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.


KEY PLAN

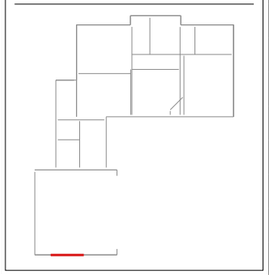

Revisions (Rev · Date · Note): **C01 - Construction issue**


Date: **2026-09-14**	Scale: **1:20**	Drawn: **TS**	Checked:
Project Name: **MP Adams Plot 4, Eckington**			
Site: **Eckington**		Client: **MP Adams**	
Title: **Panel Fabrication — 38 x 140 C16 CLS**			
Project Number: **P4**		Revision: **C01**	
Panel No: **GB-EX2**		Drawing No: **P4-MF-GB-EX2**	
Panel L×H×T: **2400×3230×149**		Weight: **334 kg**	
Status: **CONSTRUCTION**		Sheet: **1 / 1**	


Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

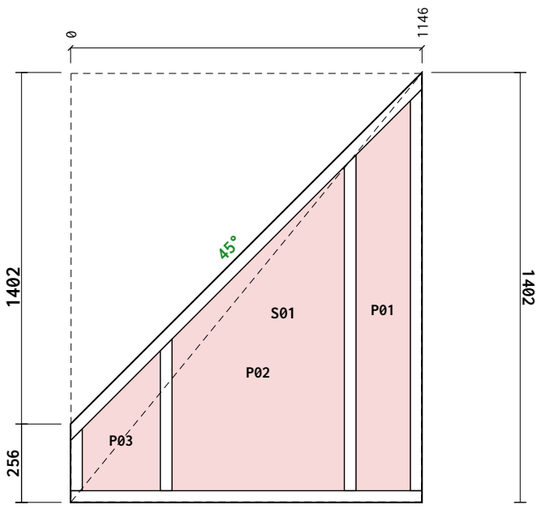

Breather bot overlap: 1298mm

Breather R overlap: 150mm





Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1146	0	0	1
TR1 Top Rail	38×140 C16	1146	0	0	1
ES1 End Stud	38×140 C16	202	0	-45.0	1
ES2 End Stud	38×140 C16	1310	0	-45.0	1
VS1 Vertical Stud	38×140 C16	1094	0	-45.0	1
VS2 Vertical Stud	38×140 C16	494	0	-45.0	1
Total: 6 pcs / 5.39 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	1143	1397	**S01**
PIR 120mm	176	1271	**P01**
PIR 120mm	561	1055	**P02**
PIR 120mm	254	455	**P03**

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.


Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN

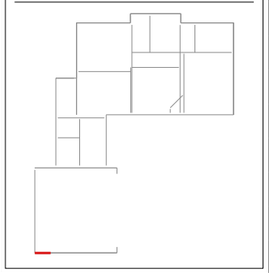


Revisions (Rev · Date · Note):	C01 - Construction issue		
Date: 2026-09-14	Scale: 1:20	Drawn: TS	Checked:
Project Name:	MP Adams Plot 4, Eckington		
Site: Eckington		Client: MP Adams	
Title:	Panel Fabrication — 38 x 140 C16 CLS		
Project Number: P4		Revision: C01	
Panel No: GB-EX3		Drawing No: P4-MF-GB-EX3	
Panel L×H×T: 1146×1402×149		Weight: 103 kg	
Status: CONSTRUCTION		Sheet: 1 / 1	


Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

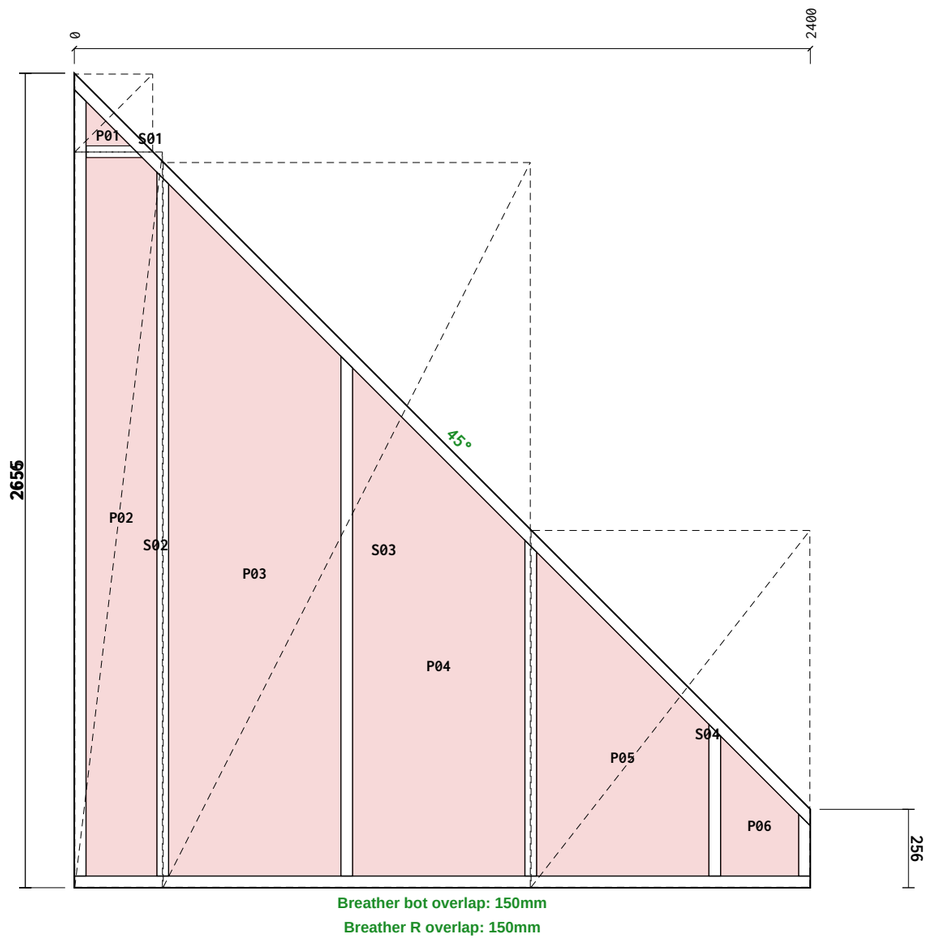

Breather bot overlap: 150mm

Breather R overlap: 150mm





Cut List

Item		Section	Len	Bot°	Top°	Qty
BR1	Bottom Rail	38×140 C16	2400	0	0	1
TR1	Top Rail	38×140 C16	2400	0	0	1
ES1	End Stud	38×140 C16	2564	0	45.0	1
ES2	End Stud	38×140 C16	202	0	45.0	1
VS1	Vertical Stud	38×140 C16	2294	0	45.0	1
VS2	Vertical Stud	38×140 C16	1694	0	45.0	1
VS3	Vertical Stud	38×140 C16	1094	0	45.0	1
VS4	Vertical Stud	38×140 C16	494	0	45.0	1
NG1	Noggin	38×140 C16	182	0	0	1

Total: 9 pcs / 13.32 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	254	254	**S01**
OSB 9mm	286	2397	**S02**
OSB 9mm	1197	2363	**S03**
OSB 9mm	909	1163	**S04**
PIR 120mm	145	144	**P01**
PIR 120mm	230	2342	**P02**
PIR 120mm	561	2255	**P03**
PIR 120mm	561	1655	**P04**
PIR 120mm	561	1055	**P05**
PIR 120mm	254	455	**P06**

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.


Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.


KEY PLAN



Revisions (Rev · Date · Note):	C01 - Construction issue		
Date: 2026-09-14	Scale: 1:20	Drawn: TS	Checked:
Project Name:	MP Adams Plot 4, Eckington		
Site: Eckington		Client: MP Adams	
Title:	Panel Fabrication — 38 x 140 C16 CLS		
Project Number: P4		Revision: C01	
Panel No: GB-EX4		Drawing No: P4-MF-GB-EX4	
Panel L×H×T: 2400×2655×149		Weight: 411 kg	
Status: CONSTRUCTION		Sheet: 1 / 1	

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

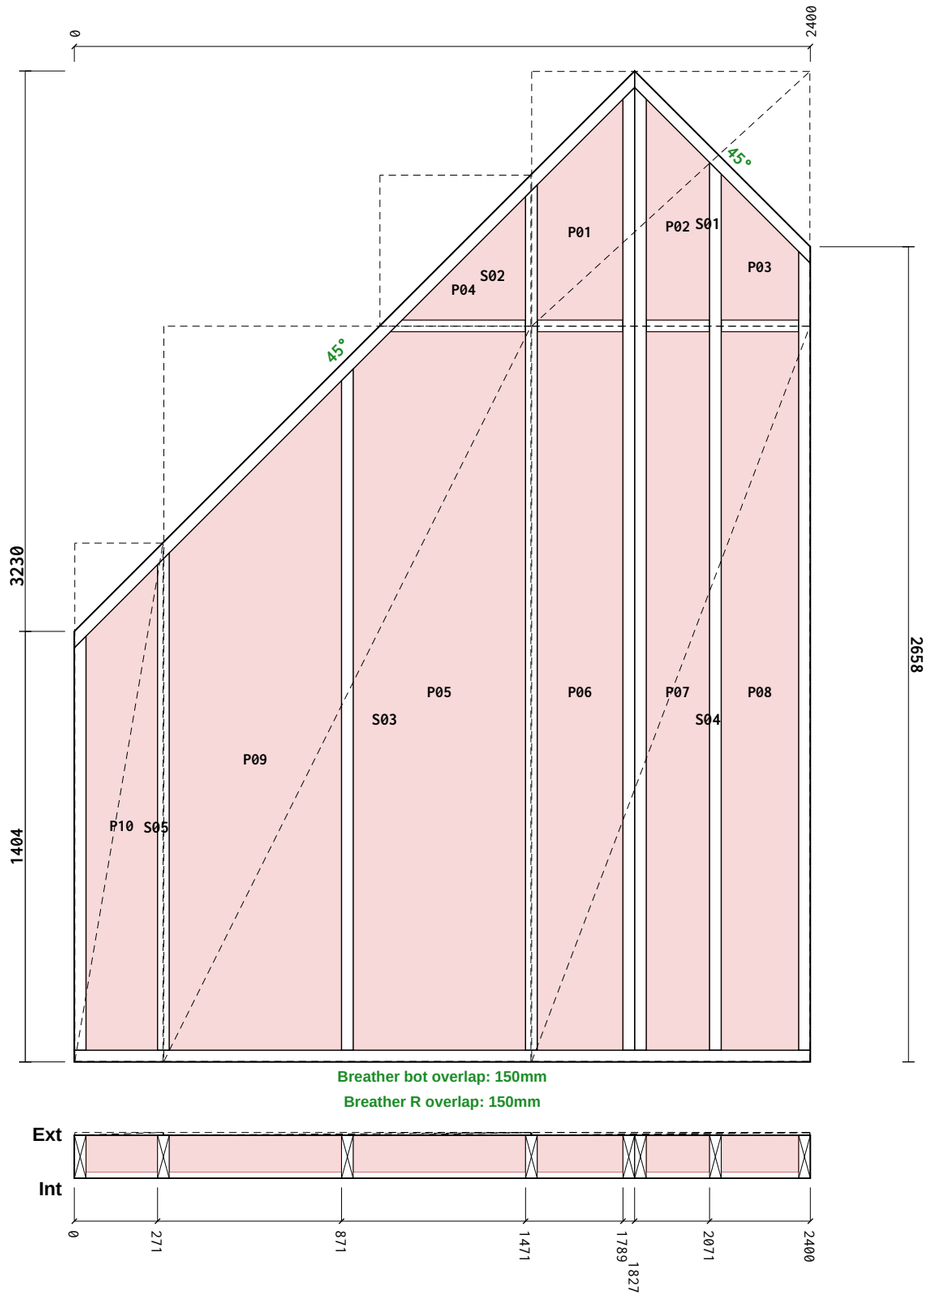



Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2400	0	0	1
TR1 Top Rail	38×140 C16	1827	0	0	1
TR2 Top Rail	38×140 C16	573	0	0	1
ES1 End Stud	38×140 C16	1350	0	-45.0	1
ES2 End Stud	38×140 C16	2604	0	45.0	1
VS1 Vertical Stud	38×140 C16	3139	0	45.0	1
VS2 Vertical Stud	38×140 C16	3139	0	-45.0	1
VS3 Vertical Stud	38×140 C16	2894	0	45.0	1
VS4 Vertical Stud	38×140 C16	2821	0	-45.0	1
VS5 Vertical Stud	38×140 C16	2221	0	-45.0	1
VS6 Vertical Stud	38×140 C16	1621	0	-45.0	1
NG1 Noggin	38×140 C16	440	0	0	1
NG2 Noggin	38×140 C16	278	0	0	1
NG3 Noggin	38×140 C16	251	0	0	1
NG4 Noggin	38×140 C16	204	0	0	1

Total: 15 pcs / 25.76 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	907	830	**S01**
OSB 9mm	492	492	**S02**
OSB 9mm	1197	2397	**S03**
OSB 9mm	907	2397	**S04**
OSB 9mm	288	1690	**S05**
PIR 120mm	279	719	**P01**
PIR 120mm	205	719	**P02**
PIR 120mm	252	475	**P03**
PIR 120mm	402	402	**P04**
PIR 120mm	561	2342	**P05**
PIR 120mm	279	2342	**P06**
PIR 120mm	205	2342	**P07**
PIR 120mm	252	2342	**P08**
PIR 120mm	561	2182	**P09**
PIR 120mm	232	1582	**P10**

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.


Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN

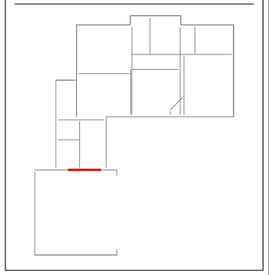


Revisions (Rev · Date · Note):	C01 - Construction issue		
Date: 2026-09-14	Scale: 1:20	Drawn: TS	Checked:
Project Name:	MP Adams Plot 4, Eckington		
Site: Eckington		Client: MP Adams	
Title:	Panel Fabrication — 38 x 140 C16 CLS		
Project Number: P4		Revision: C01	
Panel No: GB-EX5		Drawing No: P4-MF-GB-EX5	
Panel L×H×T: 2400×3230×149		Weight: 333 kg	
Status: CONSTRUCTION		Sheet: 1 / 1	

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

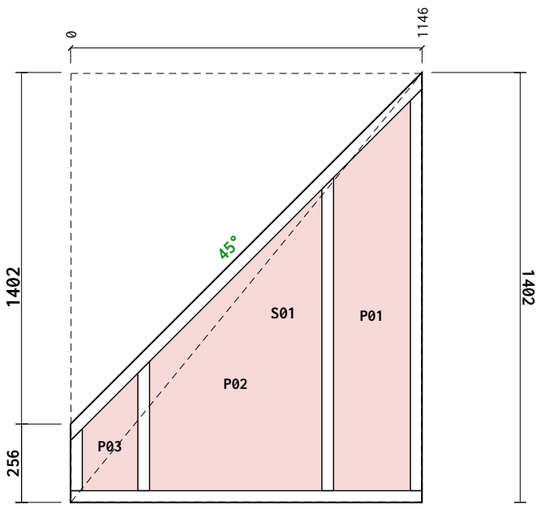

Breather bot overlap: 1298mm

Breather R overlap: 150mm





Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1146	0	0	1
TR1 Top Rail	38×140 C16	1146	0	0	1
ES1 End Stud	38×140 C16	202	0	-45.0	1
ES2 End Stud	38×140 C16	1310	0	-45.0	1
VS1 Vertical Stud	38×140 C16	1021	0	-45.0	1
VS2 Vertical Stud	38×140 C16	421	0	-45.0	1
Total: 6 pcs / 5.25 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	1143	1397	**S01**
PIR 120mm	250	1271	**P01**
PIR 120mm	561	982	**P02**
PIR 120mm	180	382	**P03**

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.


Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN




Revisions (Rev · Date · Note):	C01 - Construction issue		
Date: 2026-09-14	Scale: 1:20	Drawn: TS	Checked:
Project Name:	MP Adams Plot 4, Eckington		
Site: Eckington		Client: MP Adams	
Title:	Panel Fabrication — 38 x 140 C16 CLS		
Project Number: P4		Revision: C01	
Panel No: GB-EX6		Drawing No: P4-MF-GB-EX6	
Panel L×H×T: 1146×1402×149		Weight: 103 kg	
Status: CONSTRUCTION		Sheet: 1 / 1	


Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

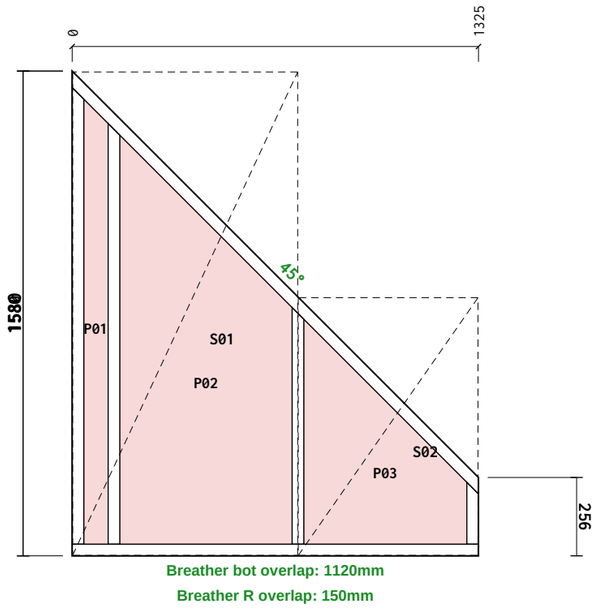

Breather bot overlap: 1120mm

Breather R overlap: 150mm





Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1325	0	0	1
TR1 Top Rail	38×140 C16	1325	0	0	1
ES1 End Stud	38×140 C16	1489	0	45.0	1
ES2 End Stud	38×140 C16	202	0	45.0	1
VS1 Vertical Stud	38×140 C16	1371	0	45.0	1
VS2 Vertical Stud	38×140 C16	771	0	45.0	1
Total: 6 pcs / 6.48 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	734	1576	**S01**
OSB 9mm	586	840	**S02**
PIR 120mm	78	1450	**P01**
PIR 120mm	561	1332	**P02**
PIR 120mm	531	732	**P03**

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.


Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN

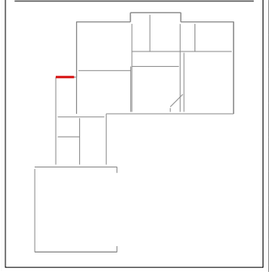


Revisions (Rev · Date · Note):	C01 - Construction issue		
Date: 2026-09-14	Scale: 1:20	Drawn: TS	Checked:
Project Name:	MP Adams Plot 4, Eckington		
Site: Eckington		Client: MP Adams	
Title:	Panel Fabrication — 38 x 140 C16 CLS		
Project Number: P4		Revision: C01	
Panel No: GB-EX7		Drawing No: P4-MF-GB-EX7	
Panel L×H×T: 1325×1580×149		Weight: 133 kg	
Status: CONSTRUCTION		Sheet: 1 / 1	

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

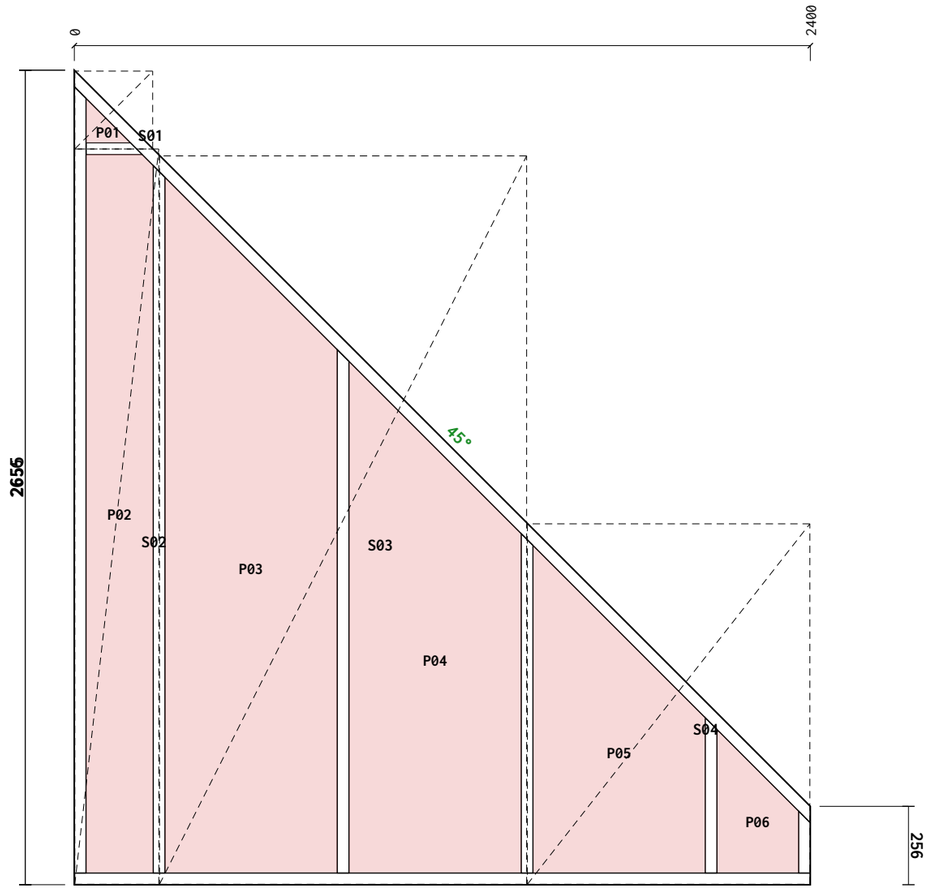


Breather bot overlap: 150mm

Breather R overlap: 150mm



Section A-A



Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2400	0	0	1
TR1 Top Rail	38×140 C16	2400	0	0	1
ES1 End Stud	38×140 C16	2564	0	45.0	1
ES2 End Stud	38×140 C16	202	0	45.0	1
VS1 Vertical Stud	38×140 C16	2306	0	45.0	1
VS2 Vertical Stud	38×140 C16	1706	0	45.0	1
VS3 Vertical Stud	38×140 C16	1106	0	45.0	1
VS4 Vertical Stud	38×140 C16	506	0	45.0	1
NG1 Noggin	38×140 C16	182	0	0	1

Total: 9 pcs / 13.37 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	254	254	**S01**
OSB 9mm	274	2397	**S02**
OSB 9mm	1197	2375	**S03**
OSB 9mm	921	1175	**S04**
PIR 120mm	145	144	**P01**
PIR 120mm	218	2342	**P02**
PIR 120mm	561	2267	**P03**
PIR 120mm	561	1667	**P04**
PIR 120mm	561	1067	**P05**
PIR 120mm	266	467	**P06**

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.


Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.


KEY PLAN

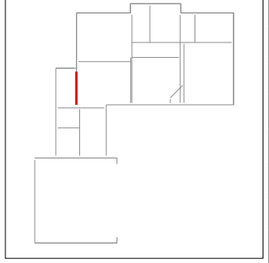

Revisions (Rev · Date · Note):	C01 - Construction issue		
Date: 2026-09-14	Scale: 1:20	Drawn: TS	Checked:
Project Name:	MP Adams Plot 4, Eckington		
Site: Eckington		Client: MP Adams	
Title:	Panel Fabrication — 38 x 140 C16 CLS		
Project Number: P4		Revision: C01	
Panel No: GB-EX8		Drawing No: P4-MF-GB-EX8	
Panel L×H×T: 2400×2655×149		Weight: 411 kg	
Status: CONSTRUCTION		Sheet: 1 / 1	

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

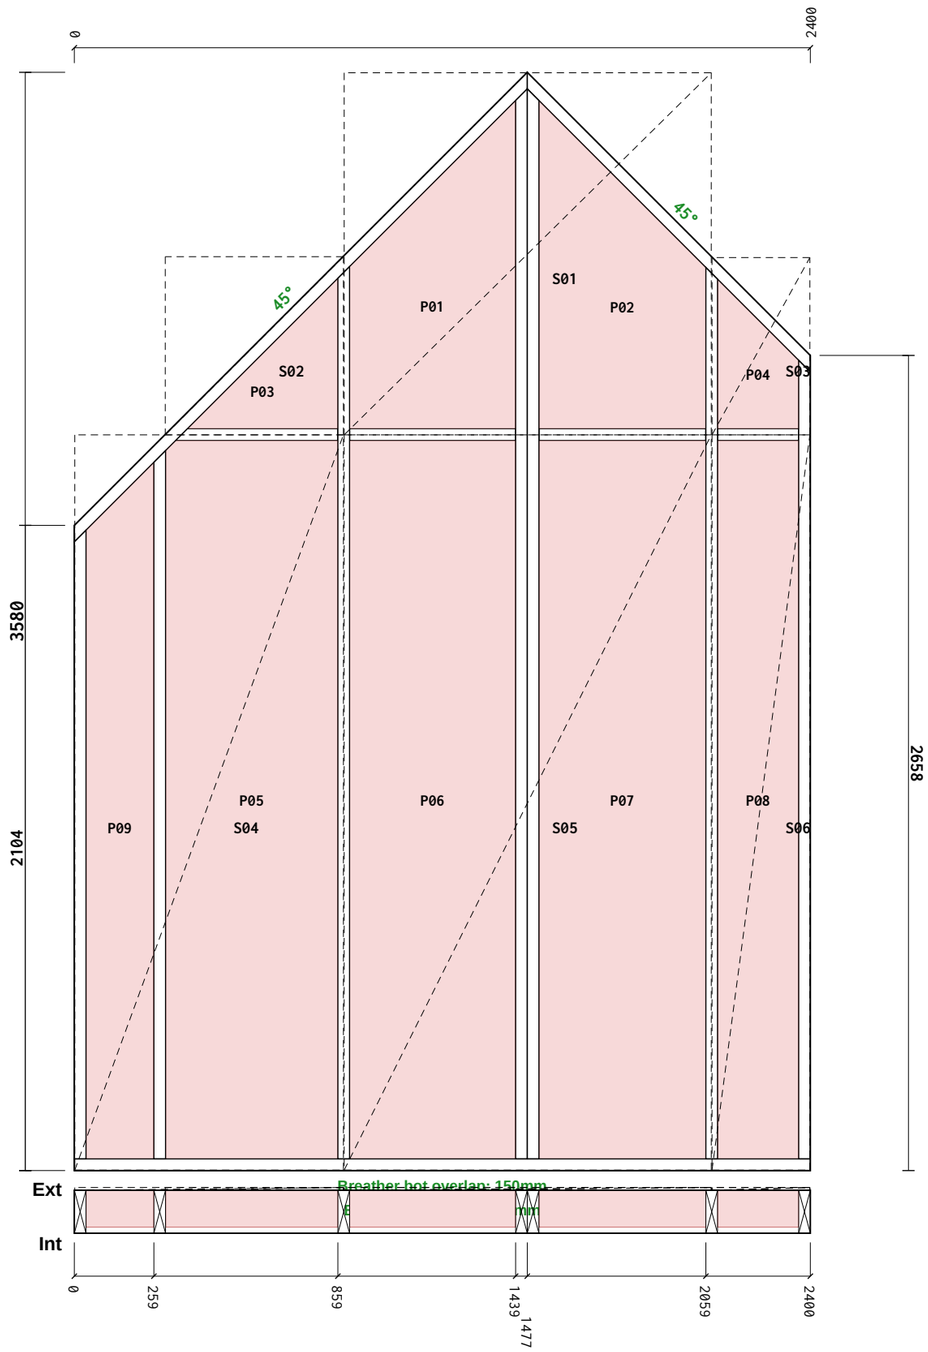



Cut List

Item		Section	Len	Bot°	Top°	Qty
BR1	Bottom Rail	38×140 C16	2400	0	0	1
TR1	Top Rail	38×140 C16	1477	0	0	1
TR2	Top Rail	38×140 C16	923	0	0	1
ES1	End Stud	38×140 C16	2050	0	-45.0	1
ES2	End Stud	38×140 C16	2604	0	45.0	1
VS1	Vertical Stud	38×140 C16	3489	0	45.0	1
VS2	Vertical Stud	38×140 C16	3489	0	-45.0	1
VS3	Vertical Stud	38×140 C16	2909	0	-45.0	1
VS4	Vertical Stud	38×140 C16	2906	0	45.0	1
VS5	Vertical Stud	38×140 C16	2309	0	-45.0	1
NG1	Noggin	38×140 C16	542	0	0	1
NG2	Noggin	38×140 C16	540	0	0	1
NG3	Noggin	38×140 C16	528	0	0	1
NG4	Noggin	38×140 C16	263	0	0	1

Total: 14 pcs / 26.43 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	1197	1181	**S01**
OSB 9mm	581	581	**S02**
OSB 9mm	319	578	**S03**
OSB 9mm	876	2397	**S04**
OSB 9mm	1197	2397	**S05**
OSB 9mm	319	2397	**S06**
PIR 120mm	541	1069	**P01**
PIR 120mm	543	1069	**P02**
PIR 120mm	490	490	**P03**
PIR 120mm	264	487	**P04**
PIR 120mm	561	2342	**P05**
PIR 120mm	541	2342	**P06**
PIR 120mm	543	2342	**P07**
PIR 120mm	264	2342	**P08**
PIR 120mm	220	2270	**P09**

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.


Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN

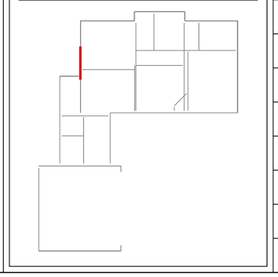


Revisions (Rev · Date · Note):	C01 - Construction issue		
Date: 2026-09-14	Scale: 1:20	Drawn: TS	Checked:
Project Name:	MP Adams Plot 4, Eckington		
Site: Eckington		Client: MP Adams	
Title:	Panel Fabrication — 38 x 140 C16 CLS		
Project Number: P4		Revision: C01	
Panel No: GB-EX9		Drawing No: P4-MF-GB-EX9	
Panel L×H×T: 2400×3580×149		Weight: 309 kg	
Status: CONSTRUCTION		Sheet: 1 / 1	


Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

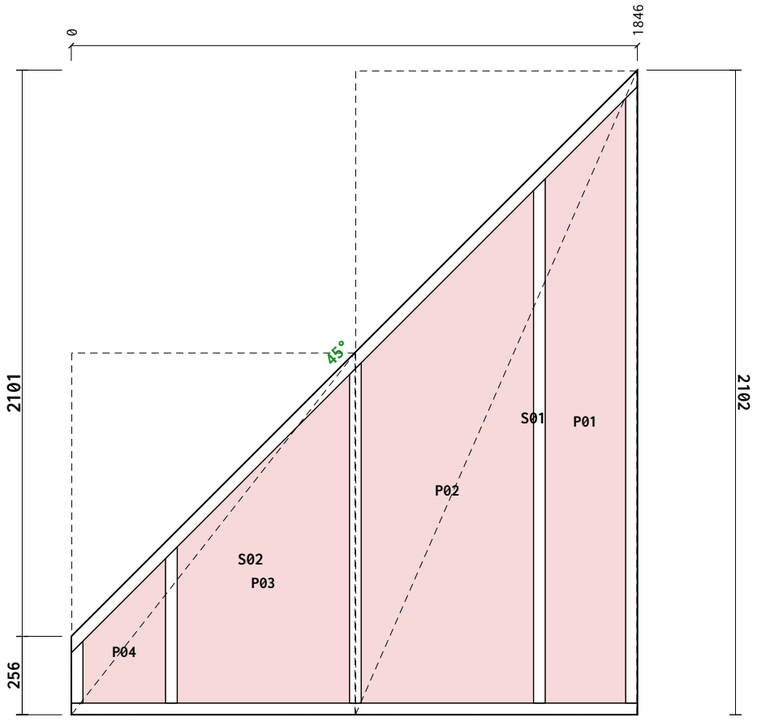

Breather bot overlap: 599mm

Breather R overlap: 150mm





Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1846	0	0	1
TR1 Top Rail	38×140 C16	1846	0	0	1
ES1 End Stud	38×140 C16	202	0	-45.0	1
ES2 End Stud	38×140 C16	2010	0	-45.0	1
VS1 Vertical Stud	38×140 C16	1709	0	-45.0	1
VS2 Vertical Stud	38×140 C16	1109	0	-45.0	1
VS3 Vertical Stud	38×140 C16	509	0	-45.0	1

Total: 7 pcs / 9.23 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	917	2097	**S01**
OSB 9mm	924	1178	**S02**
PIR 120mm	262	1971	**P01**
PIR 120mm	561	1670	**P02**
PIR 120mm	561	1070	**P03**
PIR 120mm	268	470	**P04**

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.


Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN

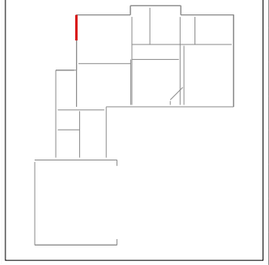


Revisions (Rev · Date · Note):	C01 - Construction issue		
Date: 2026-09-14	Scale: 1:20	Drawn: TS	Checked:
Project Name:	MP Adams Plot 4, Eckington		
Site: Eckington		Client: MP Adams	
Title:	Panel Fabrication — 38 x 140 C16 CLS		
Project Number: P4		Revision: C01	
Panel No: GB-EX10		Drawing No: P4-MF-GB-EX10	
Panel L×H×T: 1846×2101×149		Weight: 248 kg	
Status: CONSTRUCTION		Sheet: 1 / 1	


Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

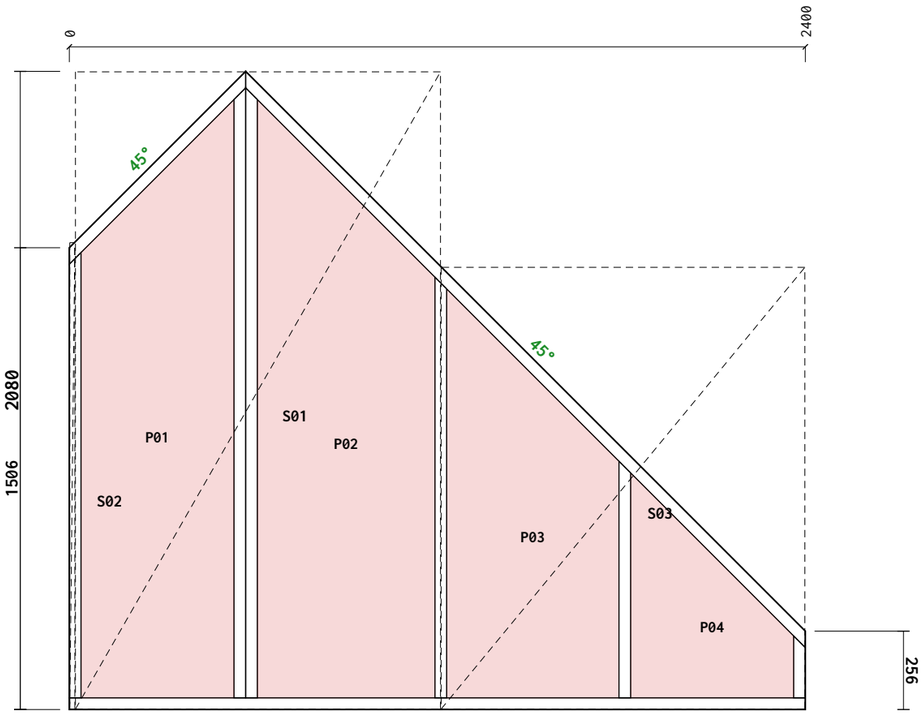

Breather bot overlap: 620mm

Breather R overlap: 150mm





Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	2400	0	0	1
TR1 Top Rail	38×140 C16	1825	0	0	1
TR2 Top Rail	38×140 C16	575	0	0	1
ES1 End Stud	38×140 C16	1452	0	-45.0	1
ES2 End Stud	38×140 C16	202	0	45.0	1
VS1 Vertical Stud	38×140 C16	1989	0	45.0	1
VS2 Vertical Stud	38×140 C16	1989	0	-45.0	1
VS3 Vertical Stud	38×140 C16	1371	0	45.0	1
VS4 Vertical Stud	38×140 C16	771	0	45.0	1

Total: 9 pcs / 12.57 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	1190	2078	**S01**
OSB 9mm	16	1520	**S02**
OSB 9mm	1186	1440	**S03**
PIR 120mm	498	1950	**P01**
PIR 120mm	578	1950	**P02**
PIR 120mm	561	1332	**P03**
PIR 120mm	531	732	**P04**

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.


Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.


KEY PLAN

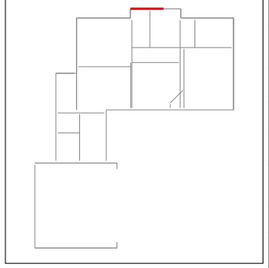


Revisions (Rev · Date · Note):	C01 - Construction issue		
Date: 2026-09-14	Scale: 1:20	Drawn: TS	Checked:
Project Name:	MP Adams Plot 4, Eckington		
Site: Eckington		Client: MP Adams	
Title:	Panel Fabrication — 38 x 140 C16 CLS		
Project Number: P4		Revision: C01	
Panel No: GB-EX11		Drawing No: P4-MF-GB-EX11	
Panel L×H×T: 2400×2080×149		Weight: 282 kg	
Status: CONSTRUCTION		Sheet: 1 / 1	

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

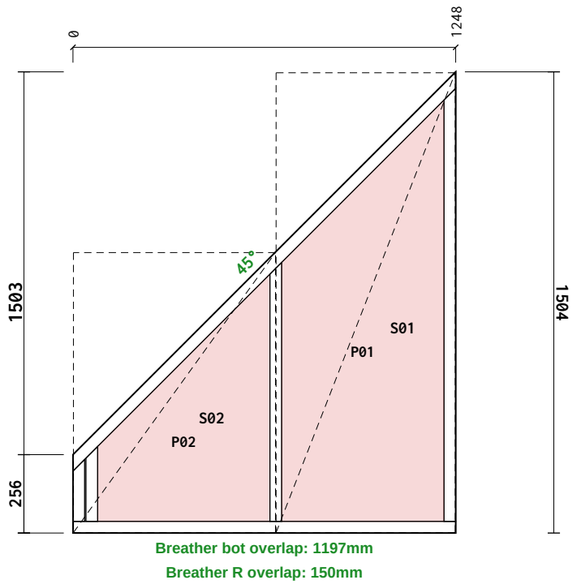





Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1248	0	0	1
TR1 Top Rail	38×140 C16	1248	0	0	1
ES1 End Stud	38×140 C16	202	0	-45.0	1
ES2 End Stud	38×140 C16	1412	0	-45.0	1
VS1 Vertical Stud	38×140 C16	844	0	-45.0	1
VS2 Vertical Stud	38×140 C16	244	0	-45.0	1
Total: 6 pcs / 5.20 m					

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	584	1499	**S01**
OSB 9mm	659	913	**S02**
PIR 120mm	529	1373	**P01**
PIR 120mm	561	805	**P02**
PIR 120mm	3	205	**P03**

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.


Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN




Revisions (Rev · Date · Note):	C01 - Construction issue		
Date: 2026-09-14	Scale: 1:20	Drawn: TS	Checked:
Project Name:	MP Adams Plot 4, Eckington		
Site: Eckington		Client: MP Adams	
Title:	Panel Fabrication — 38 x 140 C16 CLS		
Project Number: P4		Revision: C01	
Panel No: GB-EX12		Drawing No: P4-MF-GB-EX12	
Panel L×H×T: 1248×1503×149		Weight: 117 kg	
Status: CONSTRUCTION		Sheet: 1 / 1	


Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

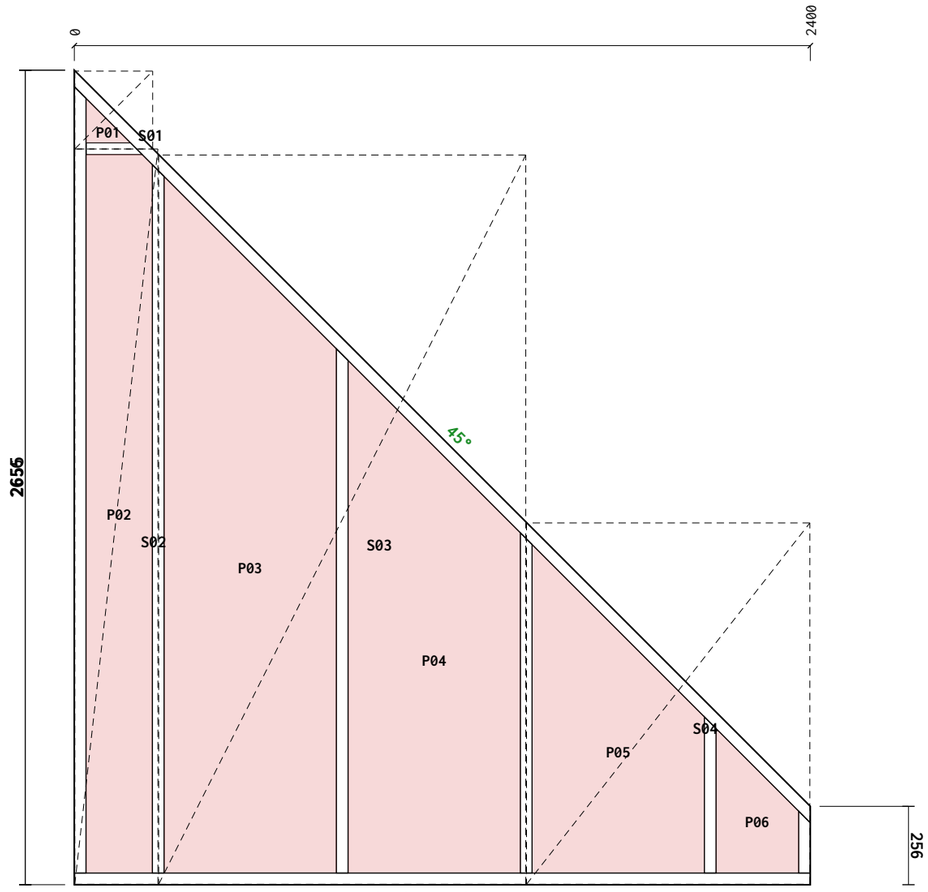

Breather bot overlap: 150mm

Breather R overlap: 150mm





Cut List

Item		Section	Len	Bot°	Top°	Qty
BR1	Bottom Rail	38×140 C16	2400	0	0	1
TR1	Top Rail	38×140 C16	2400	0	0	1
ES1	End Stud	38×140 C16	2564	0	45.0	1
ES2	End Stud	38×140 C16	202	0	45.0	1
VS1	Vertical Stud	38×140 C16	2309	0	45.0	1
VS2	Vertical Stud	38×140 C16	1709	0	45.0	1
VS3	Vertical Stud	38×140 C16	1109	0	45.0	1
VS4	Vertical Stud	38×140 C16	509	0	45.0	1
NG1	Noggin	38×140 C16	182	0	0	1

Total: 9 pcs / 13.38 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	254	254	**S01**
OSB 9mm	271	2397	**S02**
OSB 9mm	1197	2377	**S03**
OSB 9mm	924	1178	**S04**
PIR 120mm	145	144	**P01**
PIR 120mm	216	2342	**P02**
PIR 120mm	561	2270	**P03**
PIR 120mm	561	1670	**P04**
PIR 120mm	561	1070	**P05**
PIR 120mm	268	470	**P06**

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.


Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.


KEY PLAN

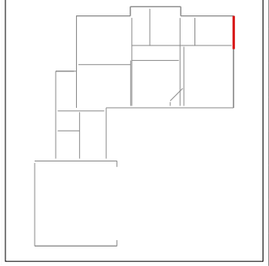

Revisions (Rev · Date · Note):	C01 - Construction issue		
Date: 2026-09-14	Scale: 1:20	Drawn: TS	Checked:
Project Name:	MP Adams Plot 4, Eckington		
Site: Eckington		Client: MP Adams	
Title:	Panel Fabrication — 38 x 140 C16 CLS		
Project Number: P4		Revision: C01	
Panel No: GB-EX13		Drawing No: P4-MF-GB-EX13	
Panel L×H×T: 2400×2655×149		Weight: 411 kg	
Status: CONSTRUCTION		Sheet: 1 / 1	

Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

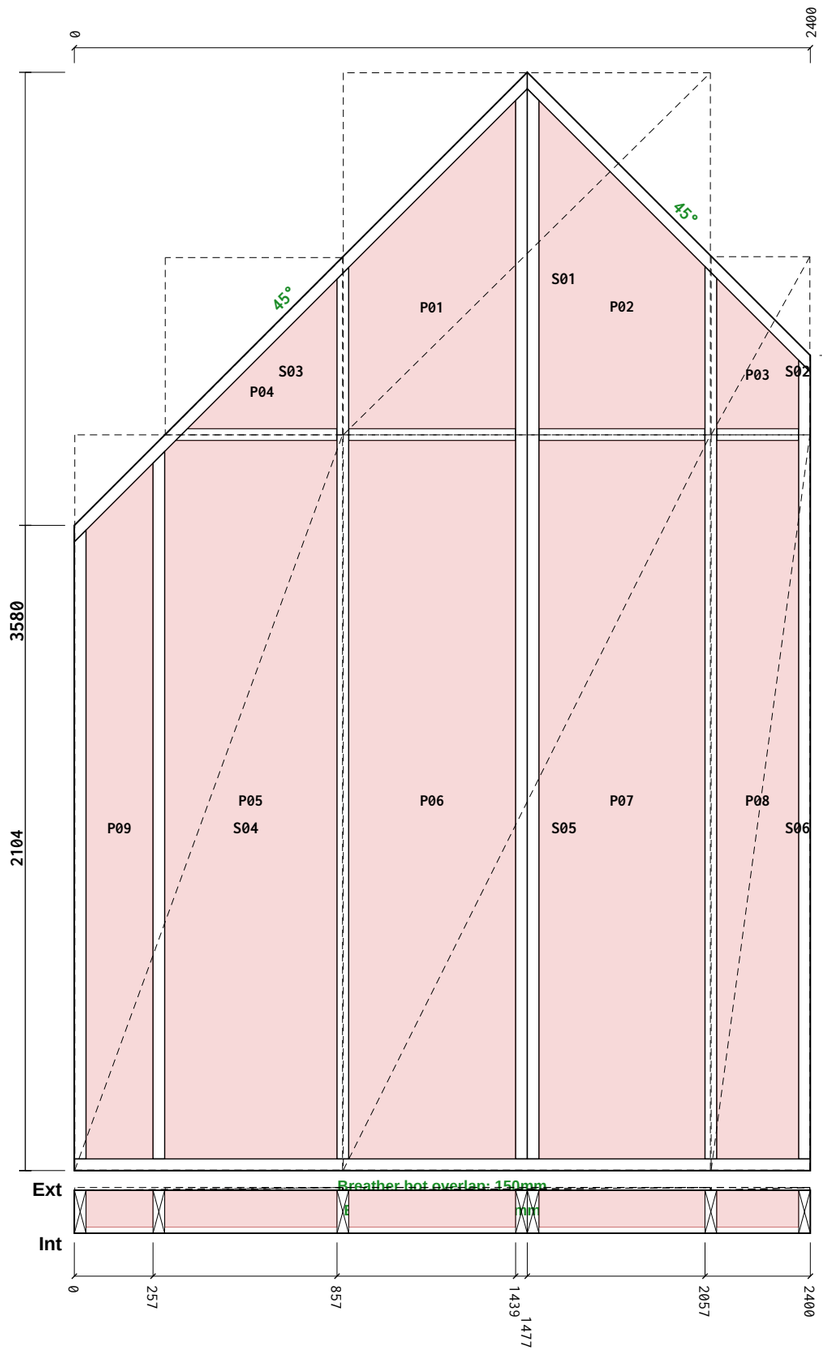



Cut List

Item		Section	Len	Bot°	Top°	Qty
BR1	Bottom Rail	38×140 C16	2400	0	0	1
TR1	Top Rail	38×140 C16	1477	0	0	1
TR2	Top Rail	38×140 C16	923	0	0	1
ES1	End Stud	38×140 C16	2050	0	-45.0	1
ES2	End Stud	38×140 C16	2604	0	45.0	1
VS1	Vertical Stud	38×140 C16	3489	0	45.0	1
VS2	Vertical Stud	38×140 C16	3489	0	-45.0	1
VS3	Vertical Stud	38×140 C16	2909	0	45.0	1
VS4	Vertical Stud	38×140 C16	2906	0	-45.0	1
VS5	Vertical Stud	38×140 C16	2306	0	-45.0	1
NG1	Noggin	38×140 C16	542	0	0	1
NG2	Noggin	38×140 C16	540	0	0	1
NG3	Noggin	38×140 C16	525	0	0	1
NG4	Noggin	38×140 C16	265	0	0	1

Total: 14 pcs / 26.43 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	1197	1181	**S01**
OSB 9mm	322	581	**S02**
OSB 9mm	578	578	**S03**
OSB 9mm	873	2397	**S04**
OSB 9mm	1197	2397	**S05**
OSB 9mm	322	2397	**S06**
PIR 120mm	543	1069	**P01**
PIR 120mm	541	1069	**P02**
PIR 120mm	266	490	**P03**
PIR 120mm	487	487	**P04**
PIR 120mm	561	2342	**P05**
PIR 120mm	543	2342	**P06**
PIR 120mm	541	2342	**P07**
PIR 120mm	266	2342	**P08**
PIR 120mm	218	2267	**P09**

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.


Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN

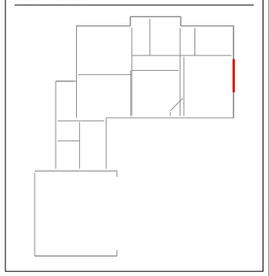


Revisions (Rev · Date · Note):	C01 - Construction issue		
Date: 2026-09-14	Scale: 1:20	Drawn: TS	Checked:
Project Name:	MP Adams Plot 4, Eckington		
Site: Eckington		Client: MP Adams	
Title:	Panel Fabrication — 38 x 140 C16 CLS		
Project Number: P4		Revision: C01	
Panel No: GB-EX14		Drawing No: P4-MF-GB-EX14	
Panel L×H×T: 2400×3580×149		Weight: 309 kg	
Status: CONSTRUCTION		Sheet: 1 / 1	


Nailing: OSB/Ply racking: 150mm perimeter / 300mm field nails (EC5 §9.2.4, 2:1 panel h:b)

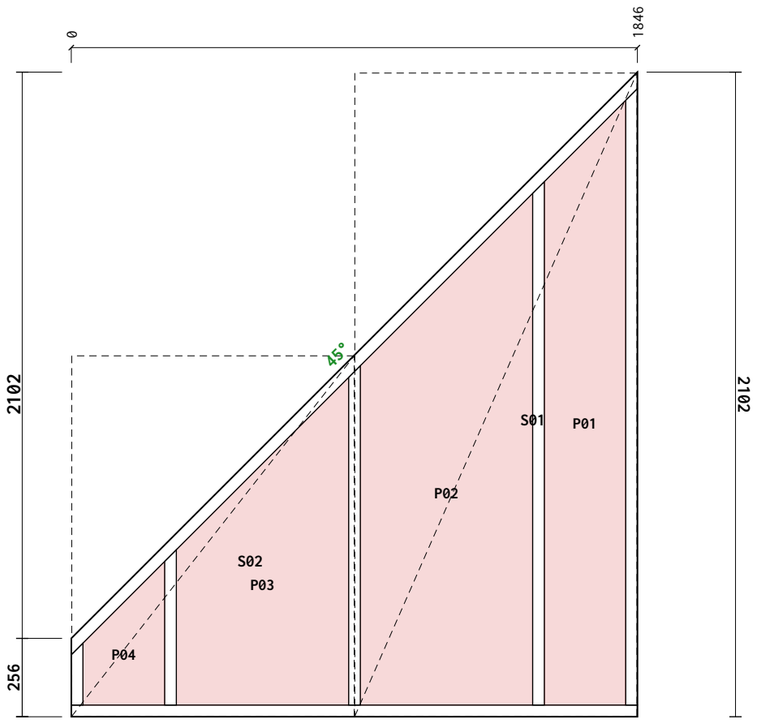

Breather bot overlap: 598mm

Breather R overlap: 150mm





Cut List

Item	Section	Len	Bot°	Top°	Qty
BR1 Bottom Rail	38×140 C16	1846	0	0	1
TR1 Top Rail	38×140 C16	1846	0	0	1
ES1 End Stud	38×140 C16	202	0	-45.0	1
ES2 End Stud	38×140 C16	2010	0	-45.0	1
VS1 Vertical Stud	38×140 C16	1706	0	-45.0	1
VS2 Vertical Stud	38×140 C16	1106	0	-45.0	1
VS3 Vertical Stud	38×140 C16	506	0	-45.0	1

Total: 7 pcs / 9.22 m

Sheathing & Insulation

Material	W	H	Label
OSB 9mm	920	2097	**S01**
OSB 9mm	921	1175	**S02**
PIR 120mm	264	1971	**P01**
PIR 120mm	561	1667	**P02**
PIR 120mm	561	1067	**P03**
PIR 120mm	266	467	**P04**

General Notes:

Frame Nailing:
140mm Frames Nail Using 3no, 3.1×90mm length field galvanised twisted strip nails
90mm Frames Nail Using 2no, 3.1×90mm length field galvanised twisted strip nails

Sheathing Nails:
Components ≤ 100mm should be +/- 1mm
Components > 100mm should be +/- 1.5mm
Stepped check should be +/- 1.5mm
Sloped Opening sizes are +/-2mm


Nailing:
30x90mm Nails, 75mm Ctrs Perimeter / 150mm Ctrs Internal.

Manufacturing Tolerances:
Length ±3 · Height ±2 · Diagonals ±5 · Openings 0/+5 (mm).
Do not scale — work to figured dimensions. All dims in mm.

Breather Membrane:
Laps 100mm horizontal / 150mm vertical, upper lapping lower.

Panel Changes:
When the panel design is changed, a clean-up of the workbench, jig, and offcut tray is required before the next panel is laid out. Verify cut-list against this drawing's revision before continuing.

KEY PLAN

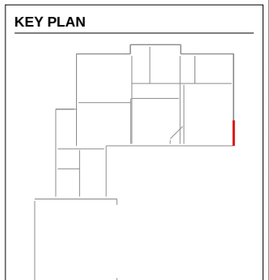

Revisions (Rev · Date · Note):	C01 - Construction issue		
Date: 2026-09-14	Scale: 1:20	Drawn: TS	Checked:
Project Name:	MP Adams Plot 4, Eckington		
Site: Eckington		Client: MP Adams	
Title:	Panel Fabrication — 38 x 140 C16 CLS		
Project Number: P4		Revision: C01	
Panel No: GB-EX15		Drawing No: P4-MF-GB-EX15	
Panel L×H×T: 1846×2102×149		Weight: 248 kg	
Status: CONSTRUCTION		Sheet: 1 / 1	
