
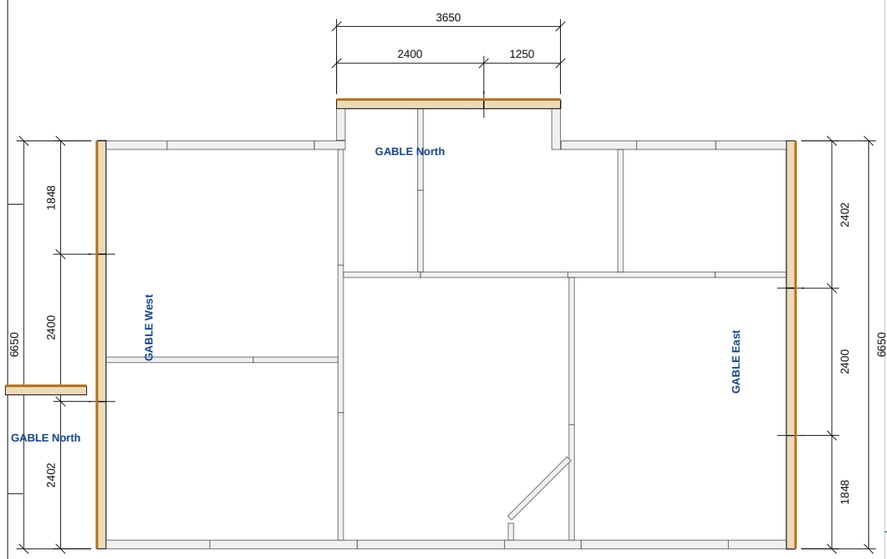


KEY PLAN - GABLES ON FIRST FLOOR WALLS


Scale 1:100 | Gable panels heavy; first floor walls below grey

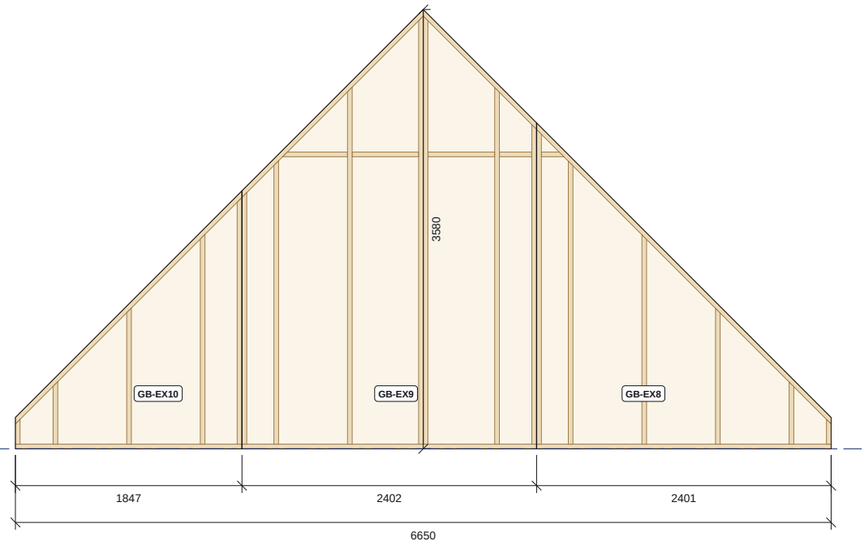

Gable base = top of first floor head binder, +5115 above slab

GABLE WEST - ELEVATION FROM OUTSIDE


Scale 1:50 | Wall 10, panels GB-EX8, GB-EX9, GB-EX10

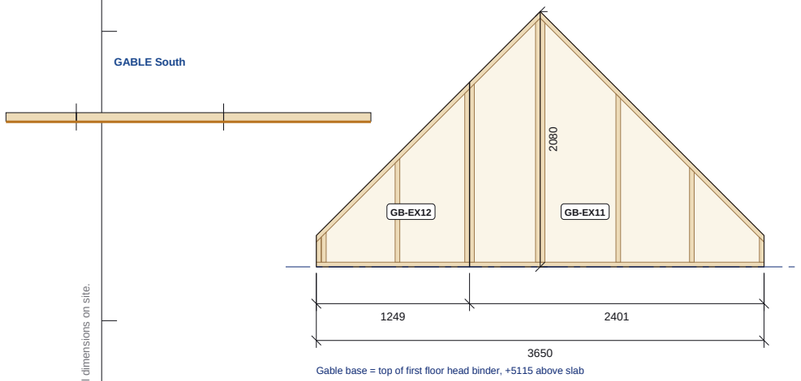

Gable base = top of first floor head binder, +5115 above slab

GABLE NORTH - ELEVATION FROM OUTSIDE

Scale 1:50 | Wall 13, panels GB-EX11, GB-EX12



Gable base = top of first floor head binder, +2462 above slab

GABLE NORTH - ELEVATION FROM OUTSIDE

Scale 1:50 | Wall 6, panels GB-EX7

GABLE PANEL SCHEDULES

GABLE PANELS

Mark	Gable	Width	Height
GB-EX8	West	2400	2656
GB-EX9	West	2400	3580
GB-EX10	West	1846	2102
GB-EX13	East	2400	2656
GB-EX14	East	2400	3580
GB-EX15	East	1846	2102
GB-EX11	North	2400	2080
GB-EX12	North	1248	1504
GB-EX1	South	2400	2656
GB-EX2	South	2400	3230
GB-EX3	South	1146	1402
GB-EX4	South	2400	2656
GB-EX5	South	2400	3230
GB-EX6	South	1146	1402
GB-EX7	North	1325	1580

Width along the wall, height to the top of the raked rail.

TEMPORARY BRACING (NOT SHOWN)

Item	No.	Order
Brace 4x1 treated rough-sawn, 2.7m	9	6 x 5.4m
Noggin 38x89 C16, 600 (nailed)	9	3 x 4.8m

One brace per gable panel joint. +5%.

NOTES

1. Gable panels: 38x140 C16 studs, 9mm OSB/3 to the external face, raked top rails to the roof pitch. No sole plate or head binder: panels bear on the first floor head binder and truss bottom chords.
2. Set out each gable from the outer edges of its central (ridge) panel to the ends of the first floor wall below, as dimensioned on the key plan.
3. Temporary bracing (not shown): one 2.7m 4x1 treated brace at every gable panel joint, fixed through a 600 38x89 noggin nailed to the deck.
4. Window battens 38x43 to gable openings: head and sill run over the jambs by 38.
5. Opening heads are measured from the underside of the panel bottom rail. Read with P4-GA-02 and P4-RF-02.

REVISIONS

REV	DATE	DESCRIPTION
C01	14.09.26	Construction issue
C02	14.09.26	Roof trusses revised; SP diagonals added

TLS TIMBER FRAME
Design & Manufacture
Scan: 3D model + drawings

CLIENT	PROJECT
MP Adams	MP Adams Plot 4, Eckington

DRAWING TITLE

GABLE PANELS GENERAL ARRANGEMENT

Key plan 1:100, gable framing elevations 1:50

SCALE	SIZE	DATE	DRAWN
1:100 / 1:50	A3	14.09.26	TS

STATUS	DRAWING No.	REV
CONSTRUCTION	P4-GA-03	C02

Do not scale. All dimensions in mm. Check all dimensions on site.
