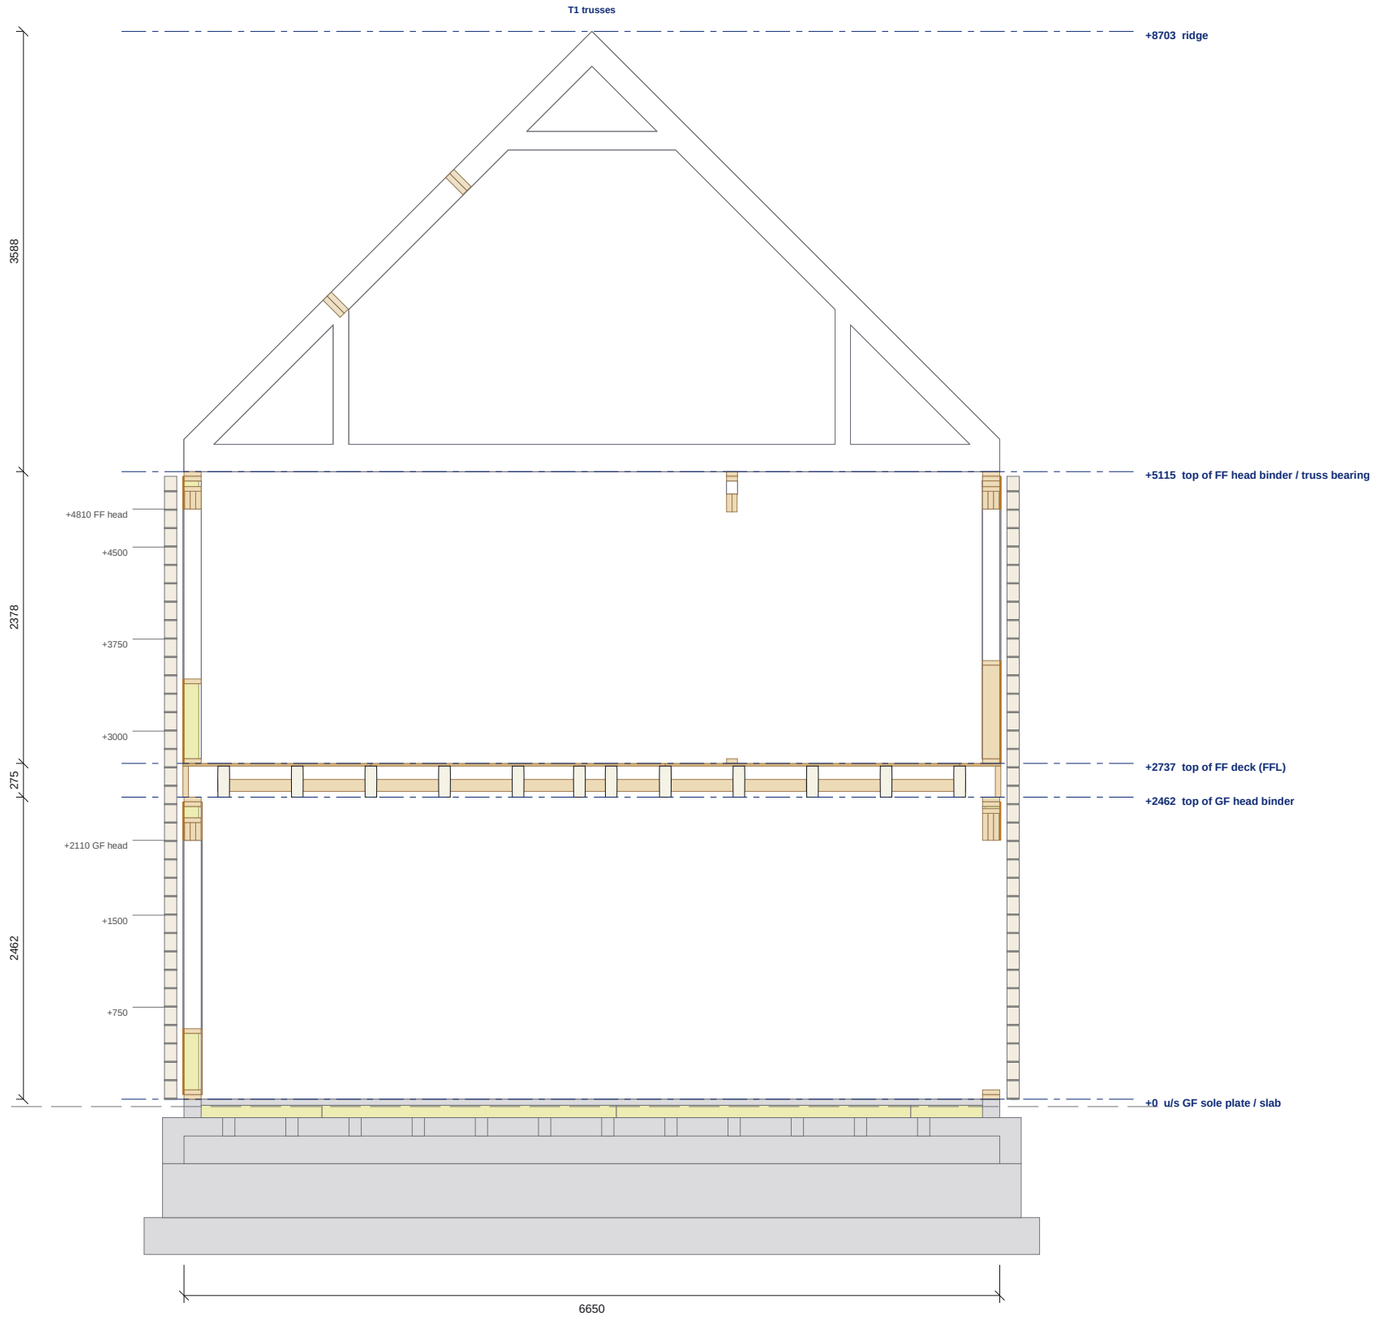


SECTION A-A

Scale 1:50 @ A3 | Main building through the lounge and master bedroom, looking west

0 1 2 3 4 5m

Do not scale. All dimensions in mm. Check all dimensions on site.

SECTION A-A SCHEDULE

LEVELS

Level	mm
u/s GF sole plate / slab	+0
top of GF head binder	+2462
top of FF deck (FFL)	+2737
top of FF head binder / truss bearing	+5115
ridge	+8703

Above underside of the ground floor sole plate.

ELEMENTS CUT

Element	Pieces cut
Sole plate / head binder	7
Panel framing	47
Edgebinder	2
22mm deck	4
Metal-web joists (Acorn)	12
Cut roof members	4
Substructure (by others)	22

NOTES

1. Section A-A cut through the timber frame model; members up to 700mm beyond the cut shown in outline.
2. Timber frame: 38x140 C16 external walls with 9mm OSB/3 and 120mm PIR; 254 metal-web first floor (Acorn); attic trusses over.
3. Stone coursing 150 (10 bed + 140) from FFL; course lines drawn on the external leaf outside the frame faces.
4. Levels are above the underside of the ground floor sole plate (+0). Substructure by others, shown for reference only.

REVISIONS

REV	DATE	DESCRIPTION
C01	14.09.26	Construction issue
C02	14.09.26	Roof trusses revised; SP diagonals added
C03	11.10.26	FF windows coursed; steel + GP1 portal; steel drawings (ST)

TLS TIMBER FRAME DESIGN SUITE

TLS TIMBER FRAME
Design & Manufacture
Scan: 3D model + drawings

CLIENT	PROJECT
MP Adams	MP Adams Plot 4, Eckington

DRAWING TITLE

SECTION A-A

Main building through the lounge and master bedroom, looking west

SCALE	SIZE	DATE	DRAWN
1:50	A3	11.10.26	TS

STATUS	DRAWING No.	REV
CONSTRUCTION	P4-SE-01	C03
